


Project Management

10. Communication Management, Stakeholders
Management & Control Project

Contents

- Communication Management
 - Dimensions of communication
- Manage Communications
- Monitor Communications
- Manage Stakeholder Engagement
- Monitor Stakeholder Engagement
- Direct and Manage Project Work process
 - PMIS
 - 3 main components of the Direct and Manage Project Work process


Getting the word out

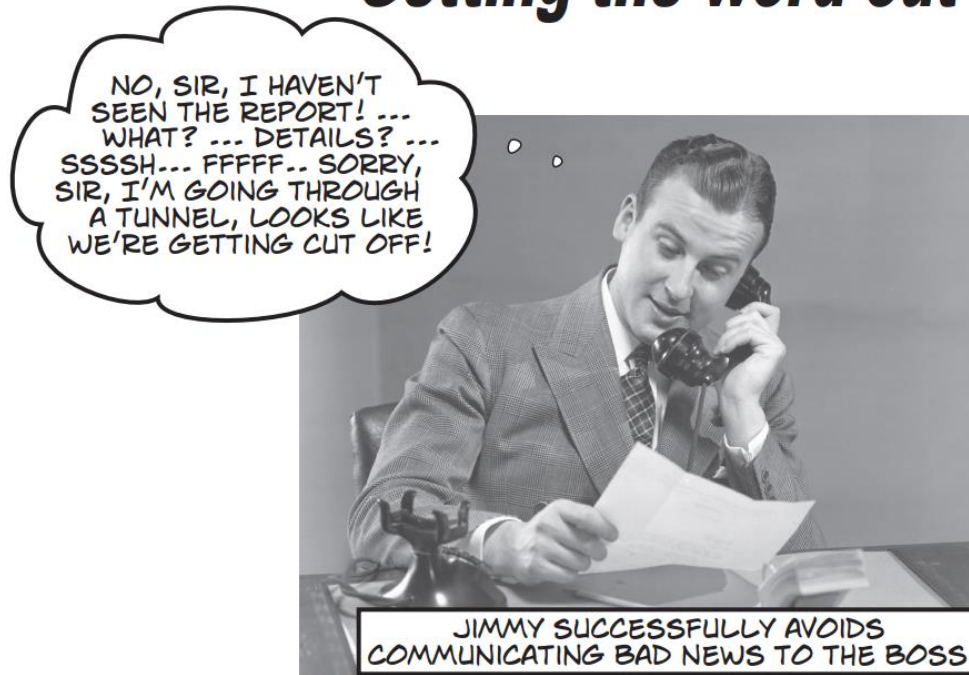

Communication Management

Communications management is about keeping everybody in the loop


Stakeholder Mngt. & Communication Mngt.

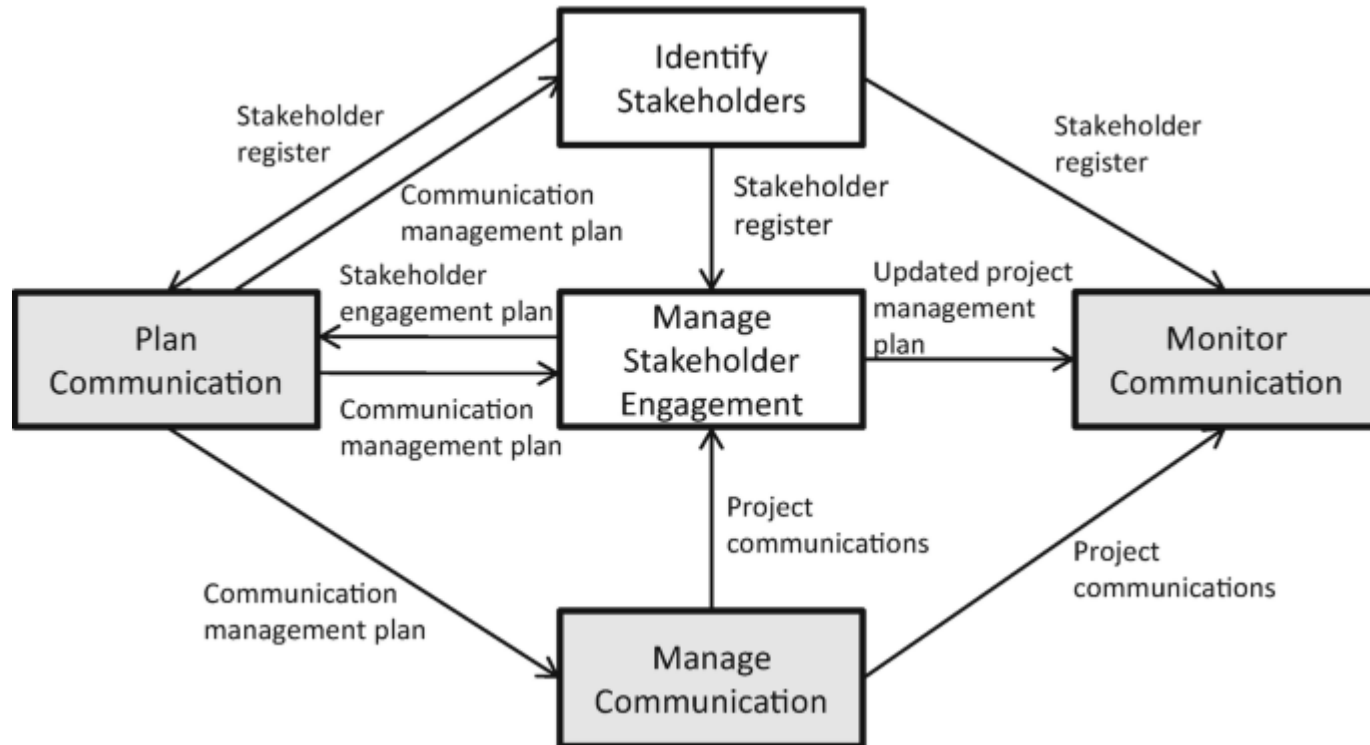

*The project manager spends **90%** of his time in communication*

What is Project Communications?

Communication is the **exchange of information**, intended or involuntary. The information exchanged can be in the form of ideas, instructions, or emotions.

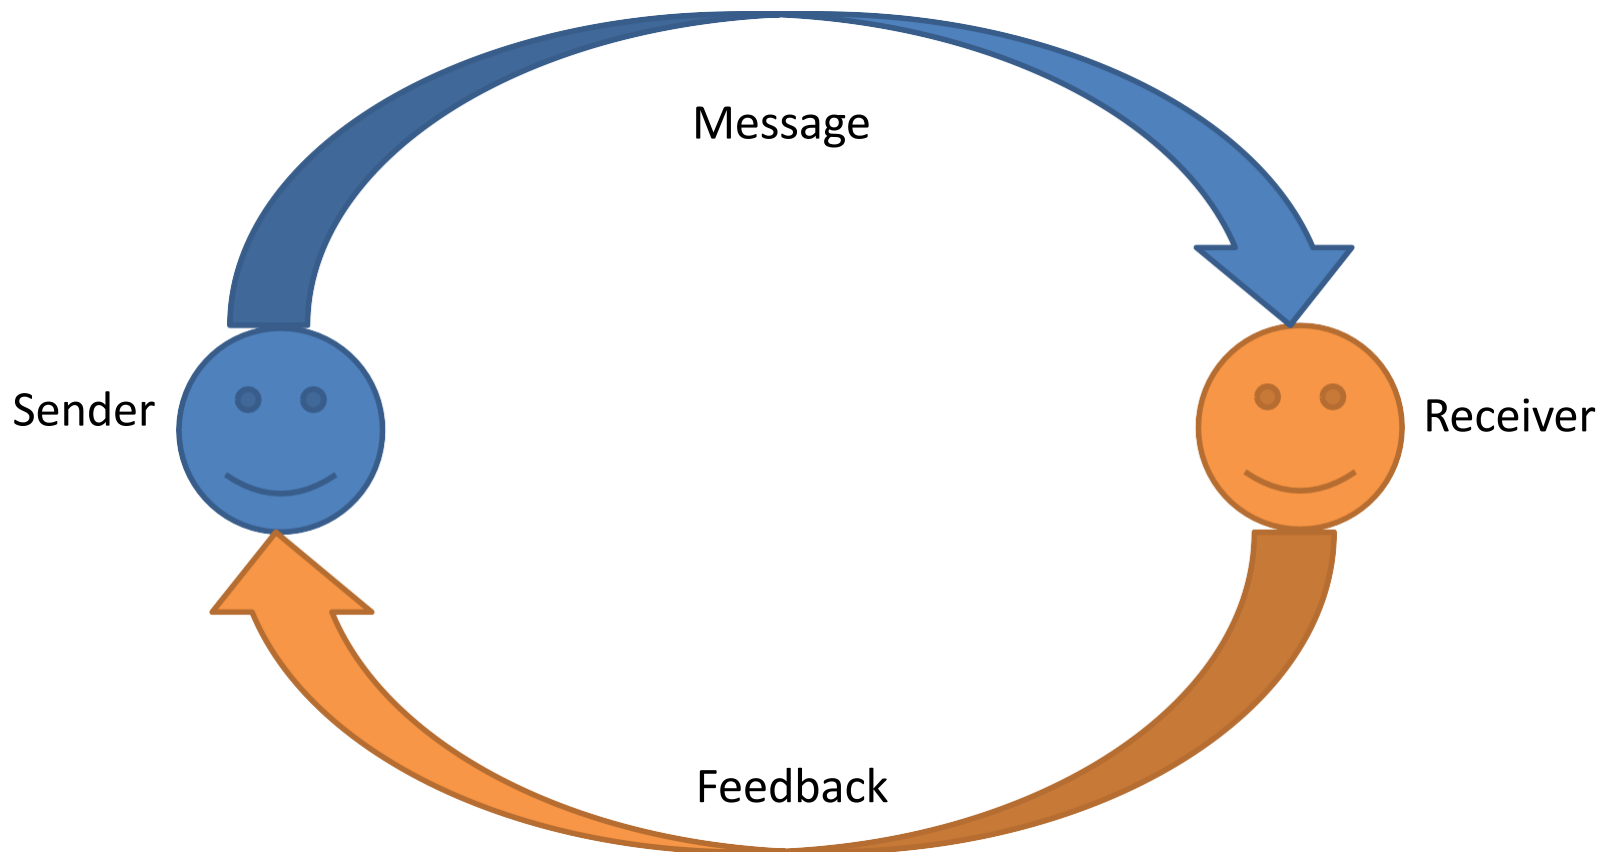

Dimensions of communication



Internal (within the project)



External (customer, vendors, other projects, organizations, the public);



Written (within the project)



Verbal (voice inflections)
and **nonverbal** (body language).

Dimensions of communication




Formal (reports, minutes, briefings)



Informal (emails, memos, ad-hoc discussions);

Level of formality, structure, and format



Official (newsletters, annual report)




Unofficial (off the record communications);

Whether it represents the organization or not

Dimensions of communication

Hierarchical focus

- **Upward:** senior management, sponsor, steering committee
- **Downward:** team members or experts
- **Horizontal**
 - **Outward:** outside the project team(suppliers, government departments, the public, end-users, and regulators)
 - **Sideward:** the peers of the project manager such as other project managers or middle managers

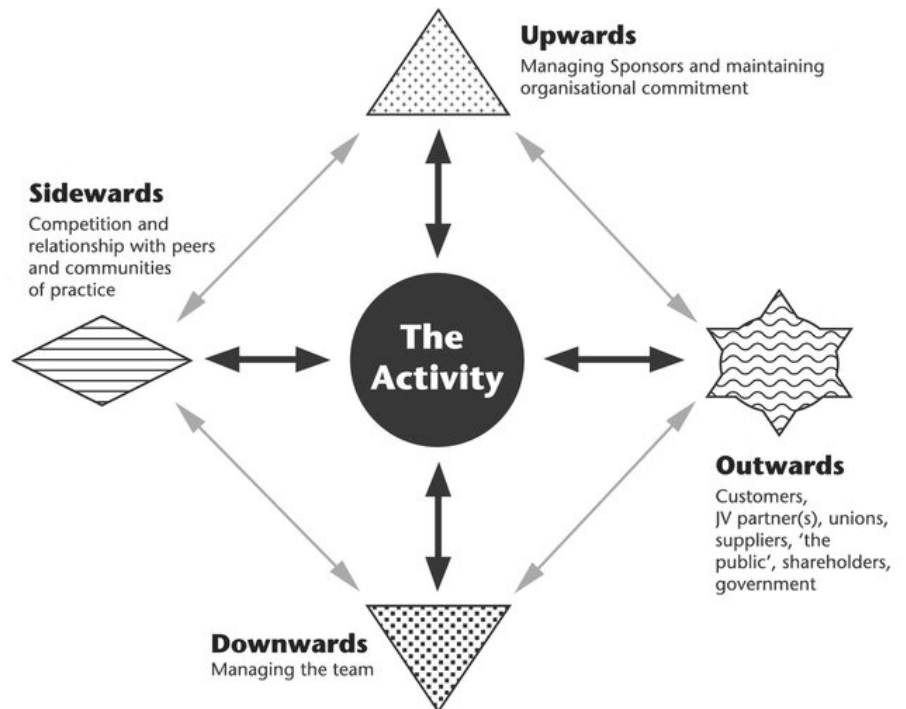

Plan Communication Management

Plan Communication Management

- **What:** developing **an appropriate approach and plan** for project communications activities based on the **information needs** of each stakeholder or group, available organizational assets, and the needs of the project.
- **Why:** *effectively* and *efficiently* engage stakeholders by presenting relevant information in a *timely* manner
- **When:** performed throughout the project as needed

Effectively & Efficiently


Productivity and optimization



Wrong audience



Delay in message delivery

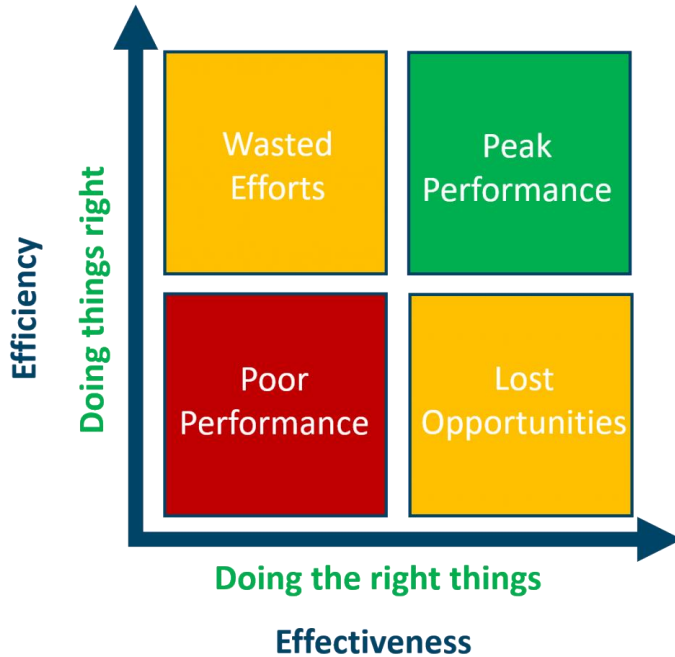


unrelevant/ Insufficient information




Results and impact

Process

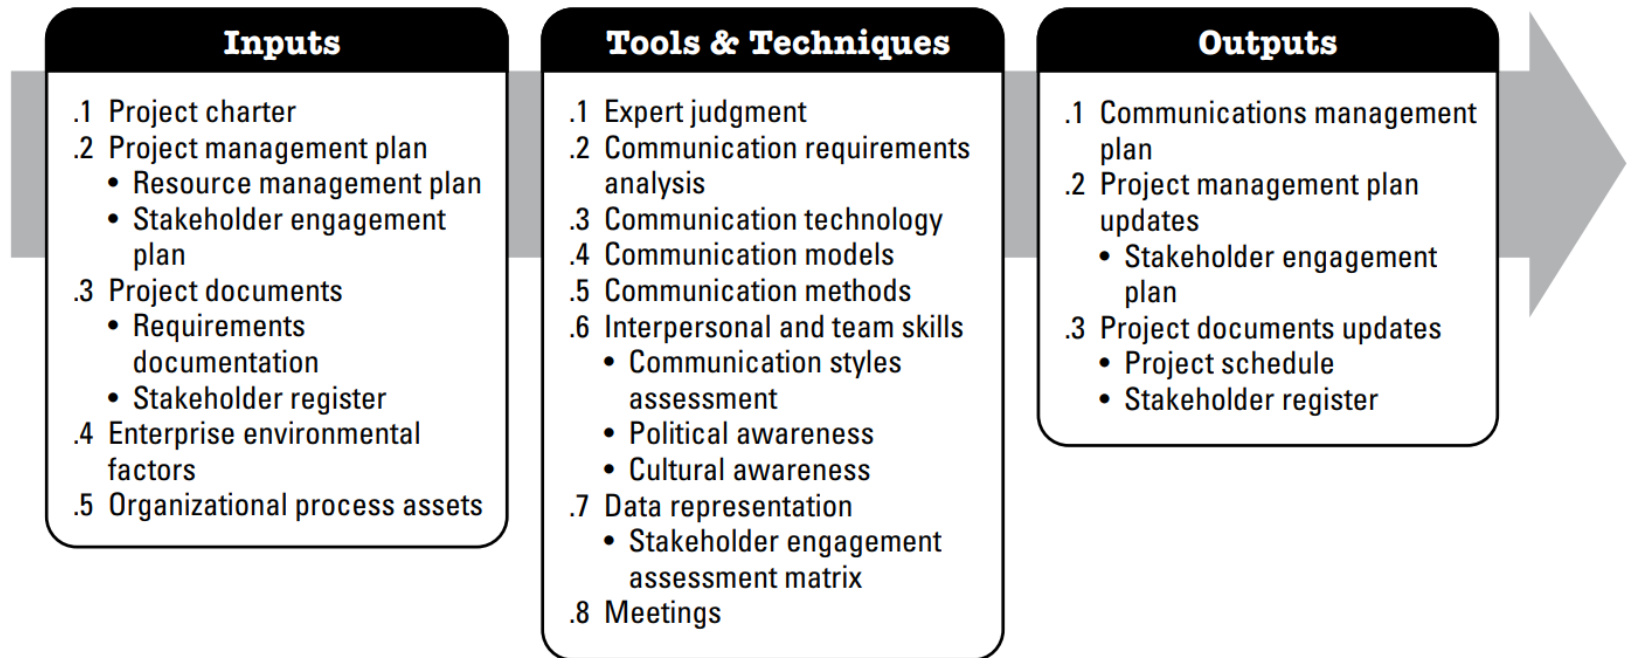

Data Flow

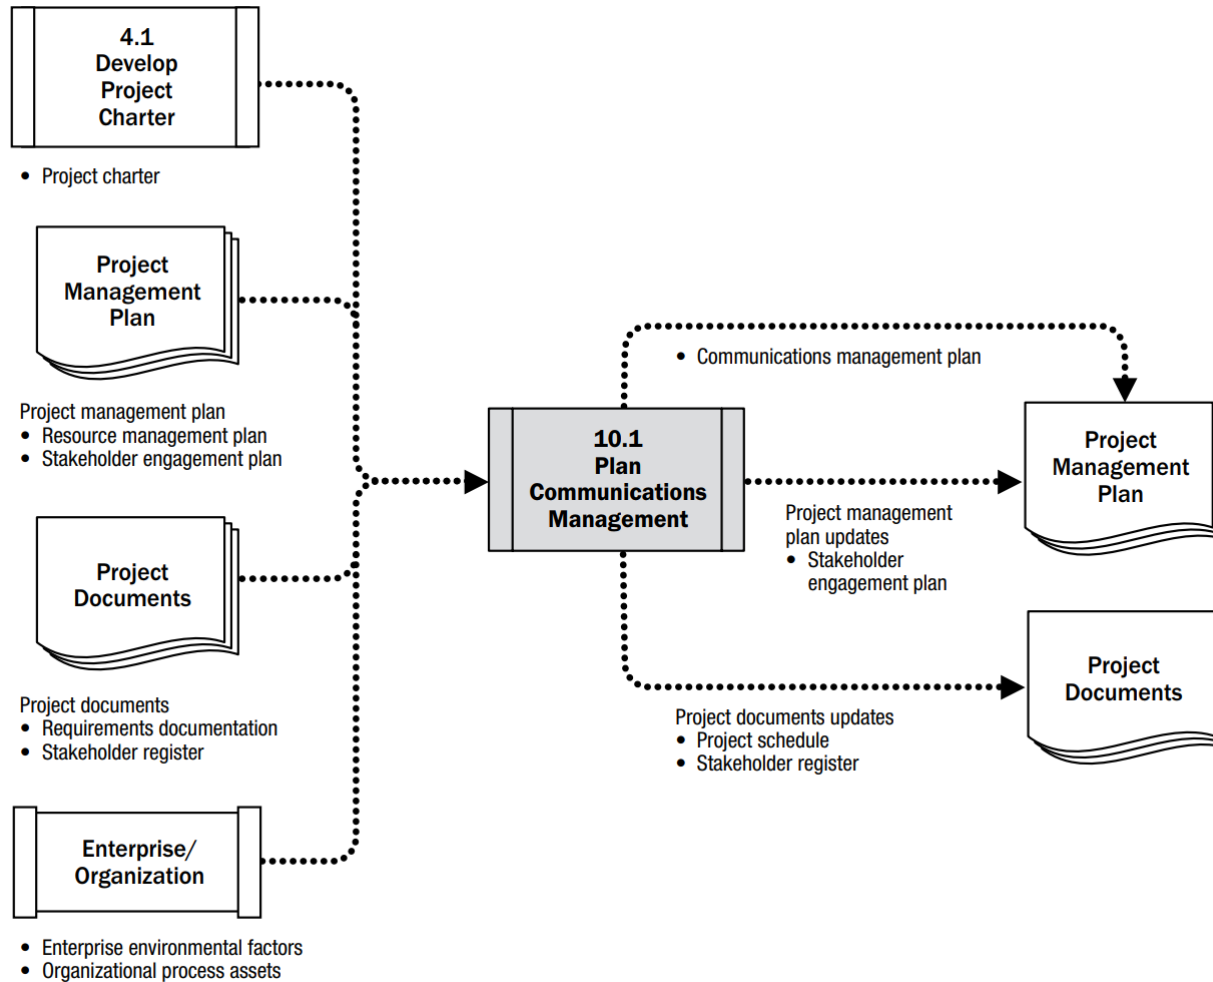


Tools & Techniques

Communication Requirement Analysis

- Stakeholder information and communication requirements (from the stakeholder register and stakeholder engagement plan)
- Project organization and stakeholder responsibility, relationships, and interdependence
- The format for communicating the information
- How often it's distributed,
- And who prepares it.

In addition, the methods of:

- Storage
- Retrieval
- And disposition of the project information

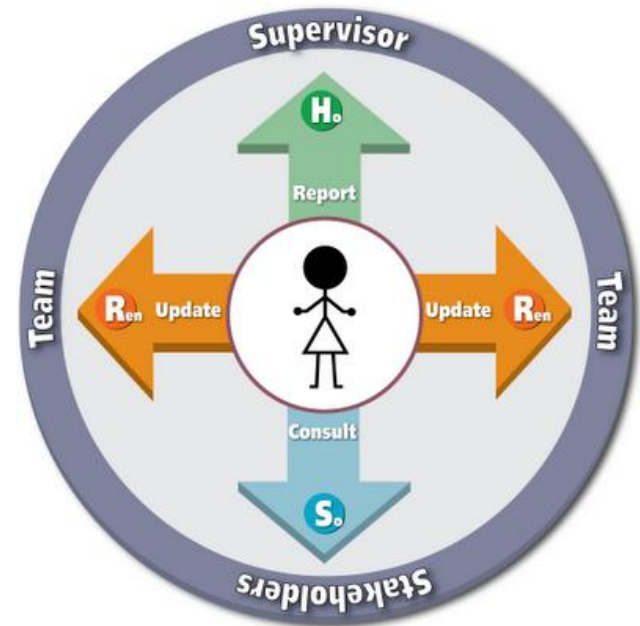

HOKOKU(報告)
REPORT TIMELY &
ADEQUATELY



RENRAKU(連絡)
COMMUNICATE
PROPERLY



SODAN(相談)
CONSULT

Tools & Techniques: Interpersonal and team skills

Communication styles assessment

Often used with unsupportive stakeholders, this assessment may follow a stakeholder engagement assessment to identify gaps in stakeholder engagement that require additional tailored communication activities and artifacts.

Political awareness

Recognition of power relationships, both formal and informal, and also the willingness to operate within these structures.


Cultural awareness

Minimize misunderstandings and miscommunication that may result from cultural differences.

Stakeholder	Unaware	Resistant	Neutral	Supportive	Leading
Stakeholder 1	C			D	
Stakeholder 2			C	D	
Stakeholder 3				D C	


Communication Technology

- As part of the communications planning, the project manager should identify all of the required and approved methods of communicating.
- Communication modalities can also include meetings, reports, memos, e- mails, and so on.

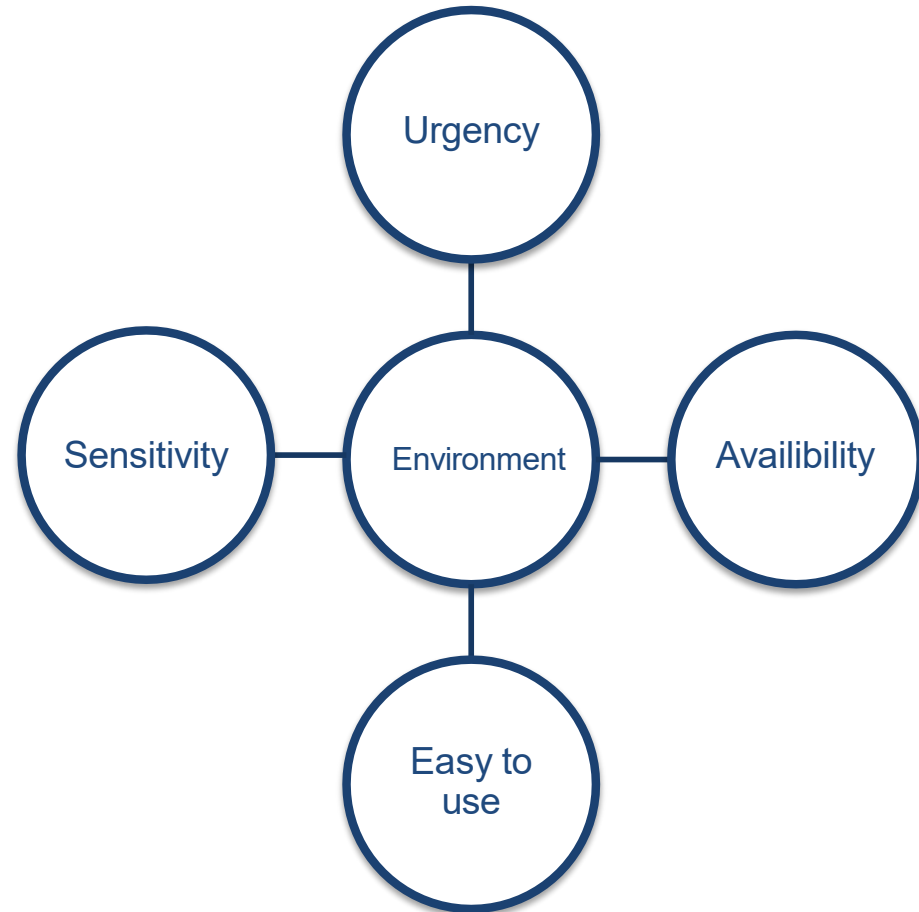

Communication model

- Communication model is appropriate for the project that is undertaken and that any barriers (noise) are identified and managed.
- Communication blockers: noise surrounding, distance, improper encoding of messages, negative attitude, language, culture.....

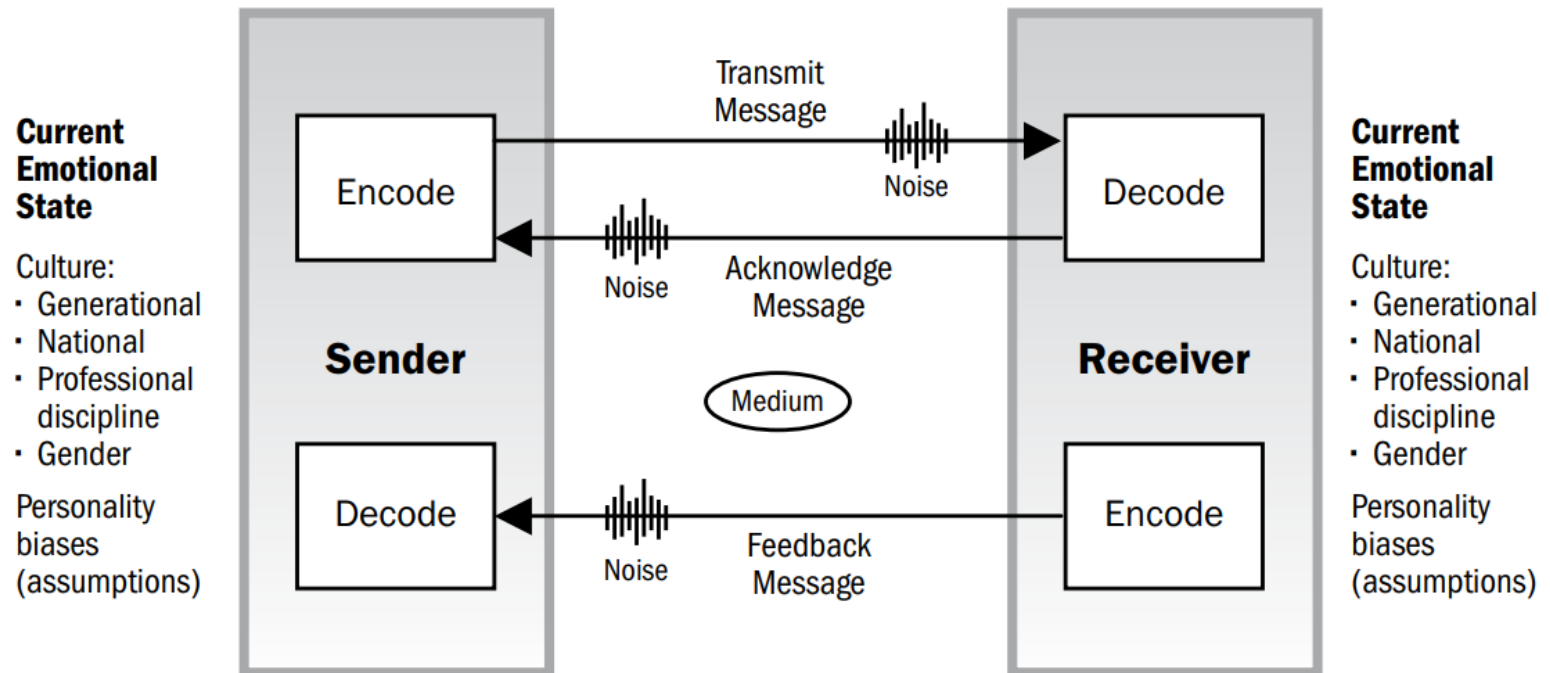

Communication model

The sender's responsibility

- Encode the message clearly
- Select a communication method
- Send the message
- Confirm that the message was understood by the receiver



The receiver's responsibility

- Make sure that the information is received in its entirety,
- Decode the message
- Confirm that the message was understood



Communication methods

- **Push communication**

- Sent a specific information to specific recipients. Examples are letters, memos, e-mails, faxes etc.
- This ensures that message is sent but will not certify that it is actually received or understood.



- **Pull communication**


- Used for large volume of information and large audiences. Examples are internet sites, company data bases, e-learning etc.
- Recipients has to access the communication content.

- **Interactive communication**

- Information are pushed and pulled in real time between two or more parties in multidirectional (Phone calls, meetings, interviews...).




Communication levels

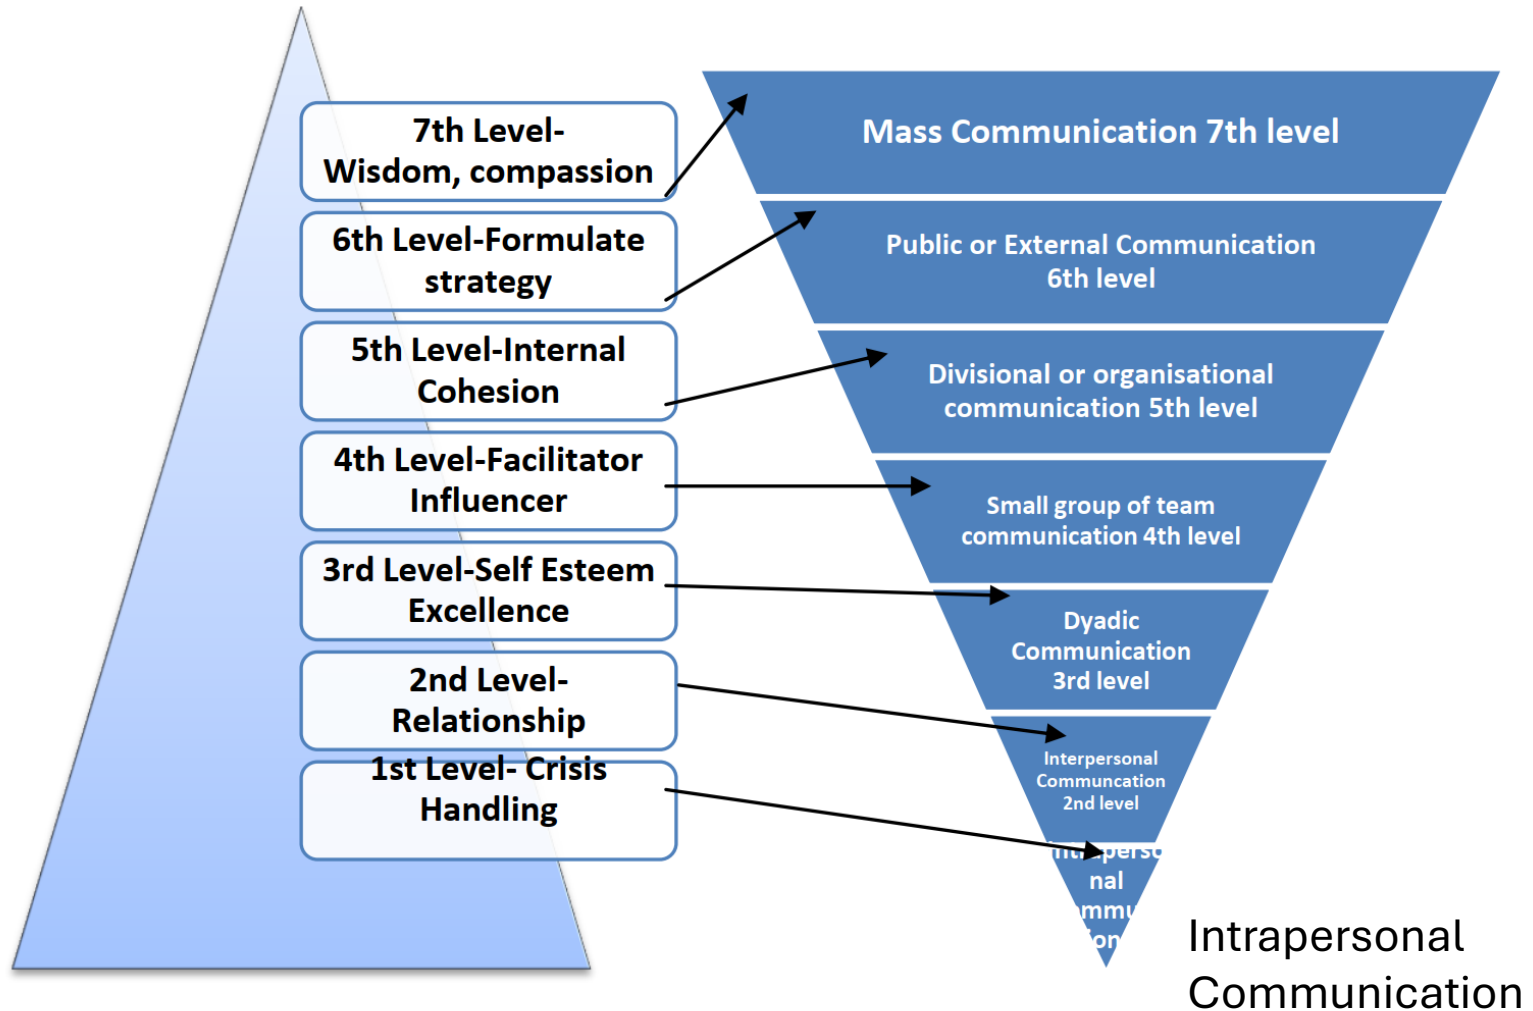

Outputs

Communications Management Plan

- Can be formal or informal,
- Highly detailed or broadly framed,
- Based on the needs of the project.
- Can include guidelines and templates for p status meetings, project team meetings, e- and email messages...



Project Management Plan Updates

- Stakeholder engagement plan

Project Document Updates

- Project schedule
- Stakeholder register: Stakeholder management strategy.

PROJECT COMMUNICATION PLAN TEMPLATE EXAMPLE

COMMUNICATION PLAN: SOFTWARE DEVELOPMENT TEAM

SUMMARY

This is the communication plan for the Atlanta software development team. It covers our schedule of meetings, where we store our shared documents, and how we communicate at other times.

COMMUNICATION GOALS

- Keep each other informed about the status of tasks (i.e., green, yellow, or red).
- Ask for and offer help where needed.
- Track budget to actual.
- Help groom the product backlog.
- Define information so you can share it with product owners and other stakeholders.

STAKEHOLDER INFORMATION

PERSON	ROLE / TITLE	CONTACT INFORMATION	COMMUNICATION FREQUENCY	FORMAT / CHANNEL	NOTES
Maria Hernández	Team Lead		Daily, weekly, monthly	The team lead facilitates the daily, in-person Scrum meeting, does weekly progress reports using Jira, and sends monthly, high-level timeline/budget/progress updates to the product owner by email.	Go-to for problem solving and questions
Jordan Oaks	Team Member - Programmer		Weekly	The team member/programmer participates in daily and weekly check-in meetings and emails.	Specializes in mobile
Wilbur Reynolds	Team Member - Programmer		Daily	The team member/programmer participates in daily and weekly check-in meetings and emails.	Oversees product backlog
David Runningbear	QA		Daily	QA reports on testing status and bug squashing.	
Sal Fiore	Release Manager		Weekly and as needed	The release manager updates release documentation.	Only person authorized to change release plan
Jennifer Planck	Product Owner		Monthly	The product owner reports team progress to leadership stakeholders monthly.	Not involved in daily Scrum meeting

COMMUNICATION TYPES

TYPE	WHEN / WHERE / PARTICIPANTS
DAILY SCRUM MEETING	We gather in person around the Scrum board for a stand-up meeting of 15 minutes.
SHARE	
• Each person reports on doing, done, to do. • Problems are flagged. • Ask for help if needed.	

TYPE	WHEN / WHERE / PARTICIPANTS
SLACK CHANNEL	This is open-ended, real-time communication and file sharing.
SHARE	
• Include the burndown chart. • Include documentation. • Ask questions so everyone can see.	


TYPE	WHEN / WHERE / PARTICIPANTS
SPRINT PLANNING AND RETROSPECTIVE	At the start and end of each two-week sprint, we meet to discuss what will be accomplished or to analyze the successes and failures of the past sprint.
SHARE	
• Share two days in advance: ◦ Agenda for meeting	

Manage Communications


Manage Communications

- **What:** ensuring *timely* and *appropriate* collection, creation, distribution, storage, retrieval, management, monitoring, and the ultimate disposition of project information.
 - distribution of relevant information
- **Why:** *efficient and effective information flow* between the project team and the stakeholders.
 - ensure that the information being communicated to project stakeholders has been appropriately generated and formatted, and received by the intended audience
 - provides opportunities for stakeholders to make requests for further information, clarification, and discussion
- **When:** performed throughout the project.

Process

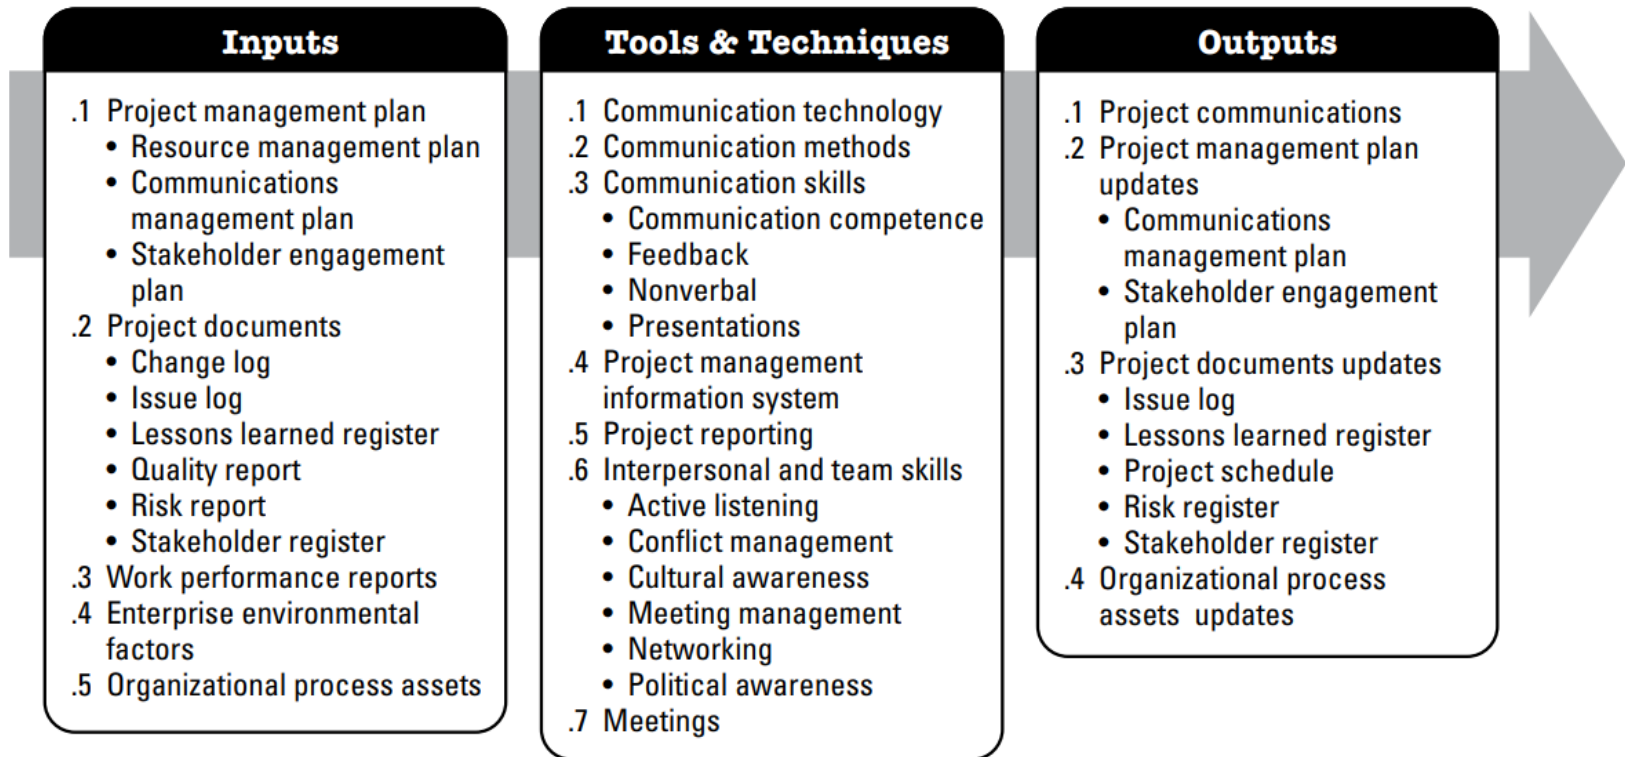

Data Flow

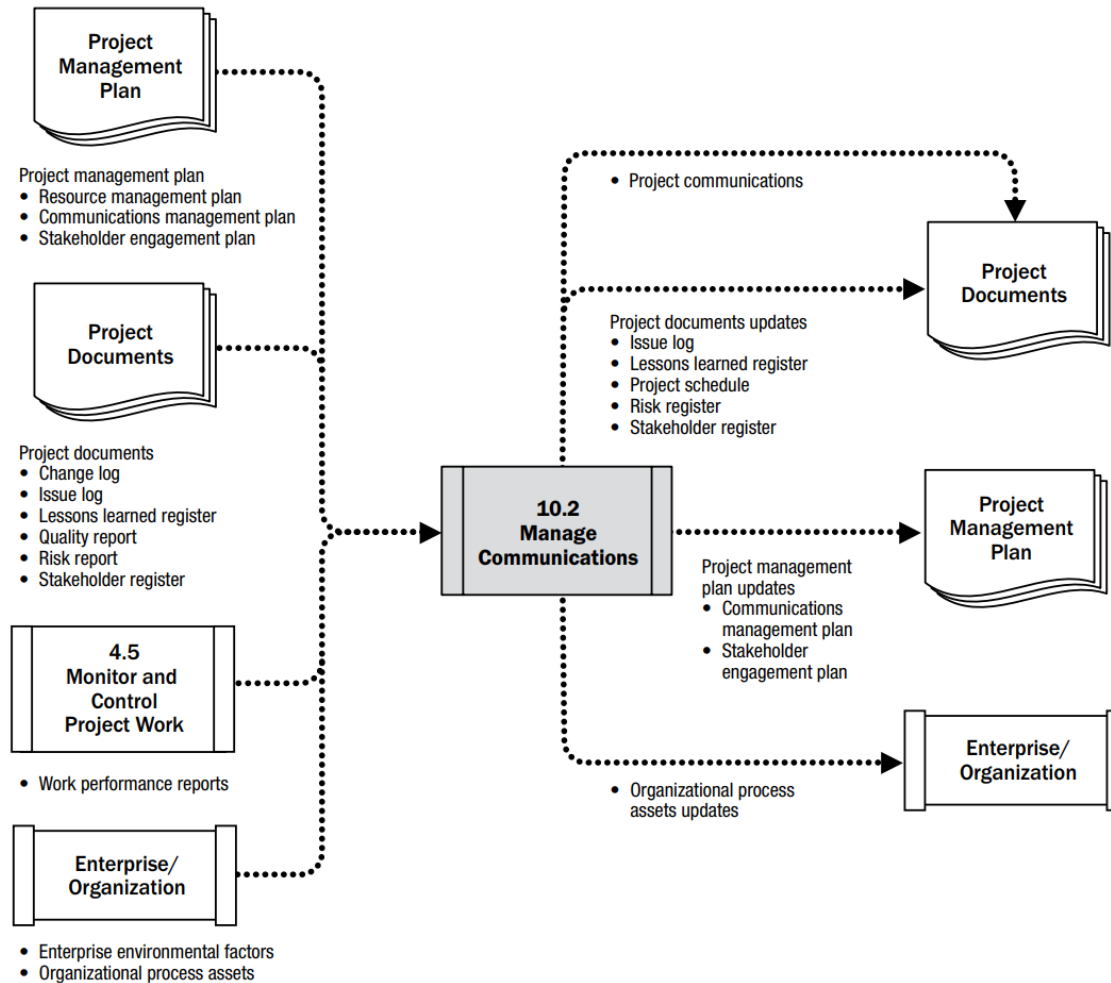

Tools & Techniques

- Techniques and considerations for effective communications
 - uSender-receiver models.
 - Choice of media
 - Writing style: Appropriate use of active versus passive voice, sentence structure, and word choice.
 - Meeting management: Preparing an agenda, inviting essential participants, and ensuring they attend. Dealing with conflicts within the meeting or resulting from inadequate follow-up of minutes and actions, or attendance of the wrong people
 - Presentations: Awareness of the impact of body language and design of visual aids.
 - Facilitation
 - Active listening.

Tools & Techniques

Communication skills

- **Communication competence:** A combination of tailored communication skills that considers factors such as clarity of purpose in key messages, effective relationships and information sharing, and leadership behaviors.
- **Feedback:** meeting, coaching, mentoring, negotiating,...
- **Nonverbal:** appropriate body language to transmit meaning through gestures, tone of voice, and facial expressions.




Tools & Techniques

Presentation


The formal delivery of information and/or documentation

- Progress reports and information updates to stakeholders;
- Background information to support decision making;
- Information about the project and its objectives.
- Take into account:
 - The audience, their expectations, and needs;
 - The needs and objectives of the project and project team.

5P's Of Presentation



7 Key Presentation Skills



Tools & Techniques

Project Information Management Systems

Tools to capture, store, and distribute information to stakeholders according to the communications plan.

- **Electronic project management tools:** web interfaces to scheduling and project management software, collaborative work management tools.
- **Electronic communications management:** e-mail, fax, voice mail, telephone,
- **Social media management:** website, blog, fanpage, online communities...



Tools & Techniques

Written communication

- **Correct grammar and spelling:** avoid distracting, distortions in the message, diminishing credibility.
- **Concise expression and elimination of excess words:** avoid misunderstanding
- **Clear purpose:** Ensure that the purpose is directed to the needs, and information is presented clearly
- **Cohesive:** Flow of ideas should be structured in logical manner
- **Complete:** Include all necessary information



Tools & Techniques

Active Listening

Listener fully concentrates, understands, responds, and remembers what the speaker is saying

- Paying full attention (no distractions).
- Showing you're listening (nodding, eye contact, encouraging words like "I see", "Go on").
- Reflecting or paraphrasing what you hear.
- Not interrupting.
- Asking clarifying questions.
- Responding thoughtfully.



Outputs

Project Communications

Project communications artifacts may include but are not limited to:

- Performance reports
- Deliverable status
- Schedule progress
- Cost incurred
- Presentations
- Information required by stakeholders

Attention!

- Any time you need to get a message to a client or sponsor, you use formal communication.
- Any project documents: project reports, requirement specification, or especially a contract: is **always formal written**.
- Meetings are **always informal verbal**, even if the meeting is to say something really important.

Outputs

Project management plan updates

- Communications management plan.
- Stakeholder engagement plan.

Project documents updates

- Stakeholder register
- Issue log,
- Risk register
- Project schedule,
- Lessons learned register

Organizational process assets updates

- Stakeholder notifications.
- Project reports.
- Project presentations.
- Project records.
- Feedback from stakeholders.
- Lessons learned documentation.

Inputs

Work Performance Reports

- Project performance and status information

Project management plan

- Stakeholder engagement plan
- **Communications management**
- Resource management plan

Project documents

- Stakeholder register
- Issue log
- Change log
- Risk report
- Quality report
- Lessons learned register

Enterprise Environmental Factors

- Organizational culture and structure,
- Government or industry standards and regulations, and
- Project management information system.

Organizational Process Assets


- Policies, procedures, processes, and guidelines regarding communications management;
- Templates; and historical information and lessons learned.

Monitor Communications


Monitor Communications

- **What:** process of ensuring the information needs of the project and its stakeholders are met.
 - determines if the planned communications artifacts and activities have had the desired effect
 - right message with the right content (the same meaning for sender and receiver) is delivered to the right audience, through the right channel, and at the right time
- **Why:** *optimal information flow* as defined in the communications management plan and the stakeholder engagement plan.
- **When:** performed throughout the project.

Process

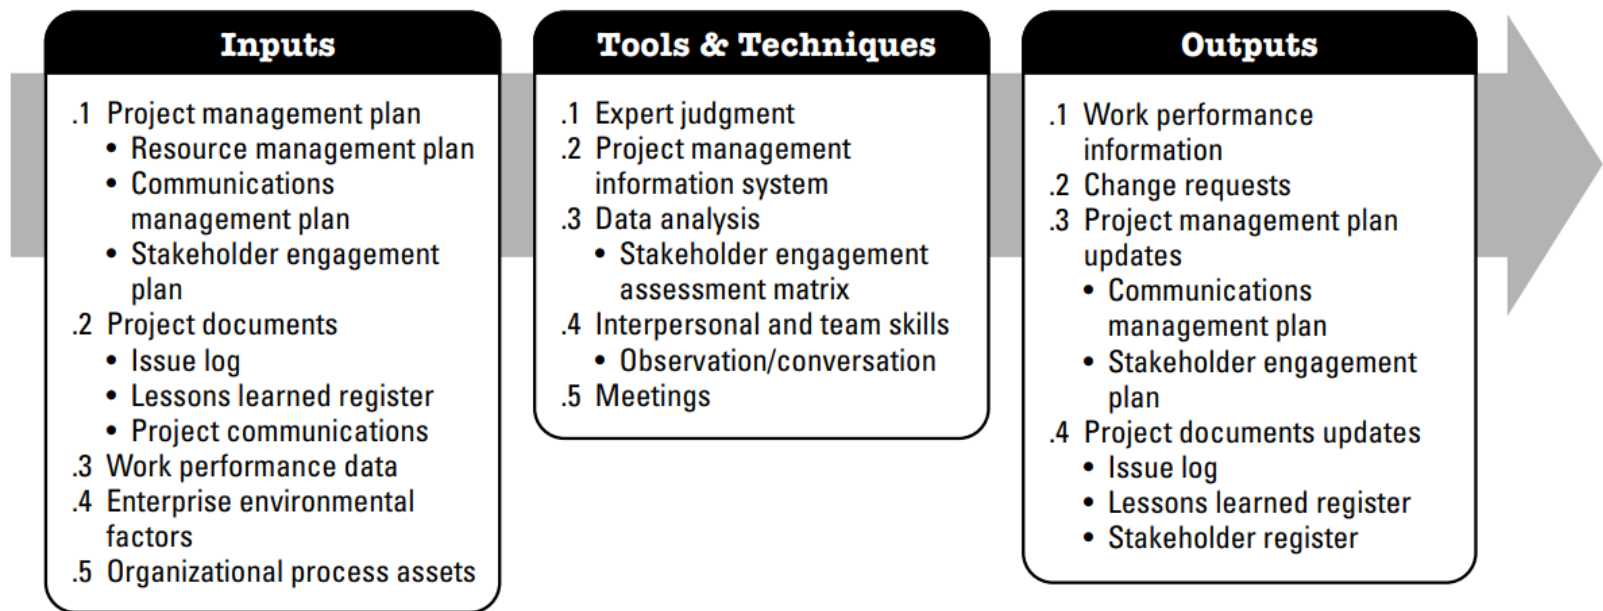

Data Flow

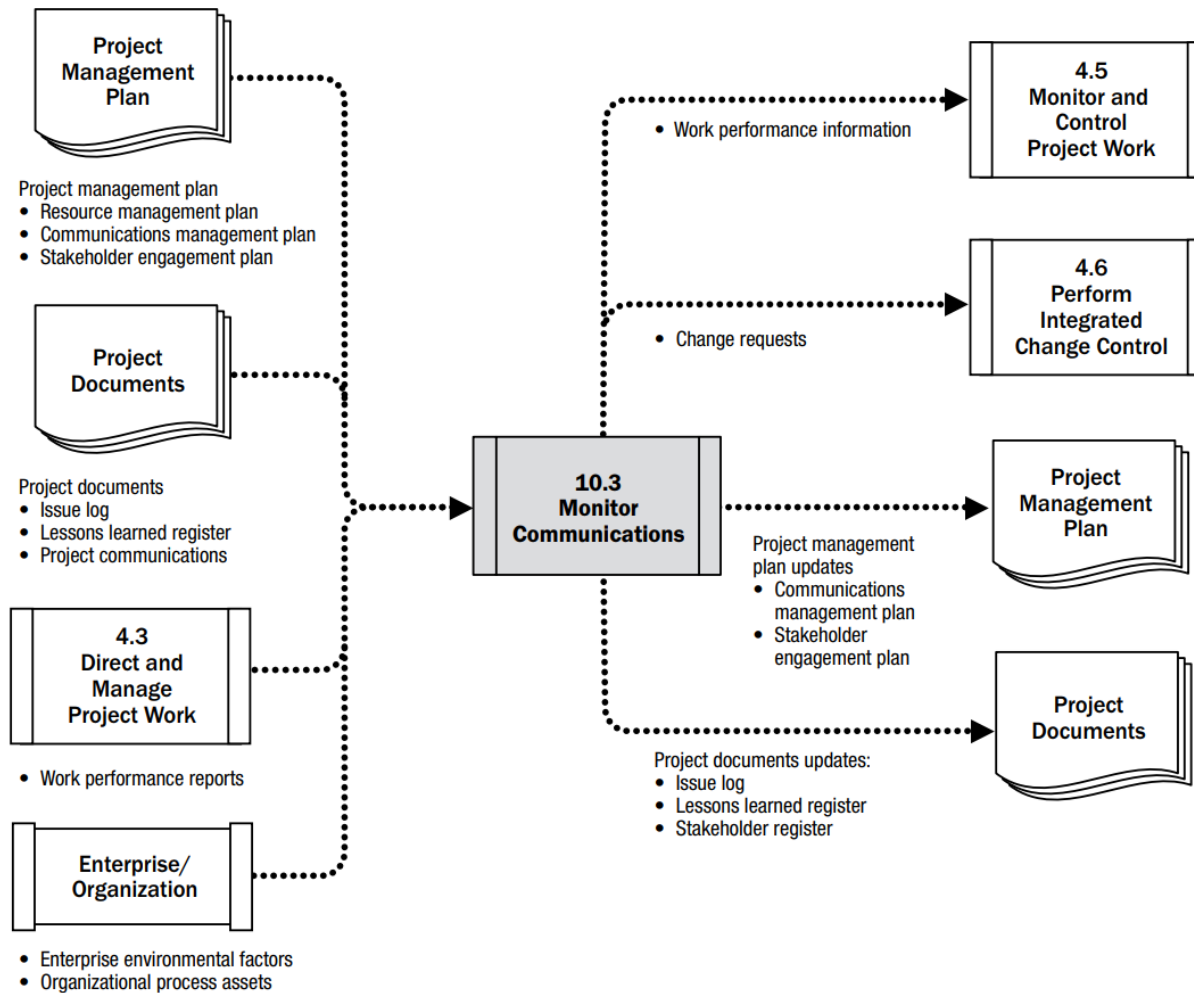

Tools & Techniques

Observation/conversation

- Observation/conversation with the project team helps determine the most appropriate way to update and communicate project performance, and to respond to requests from stakeholders for information.
- Observation/conversation enables the project manager to identify issues within the team, conflicts between people, or individual performance issues.

**Observation
Can Be More
Informative
Than
Conversation**

Tools & Techniques

Stakeholder engagement assessment matrix

- The information contained in the system is monitored to assess its validity and effectiveness.

Stakeholder	Unaware	Resistant	Neutral	Supportive	Leading
Bob	C			D	
Carol			C		D
Ted		C		D	
Alice				C,D	
Joe			C	D	

Information Management Systems

- The information contained in the system is monitored to assess its validity and effectiveness.



Outputs

Work Performance Information

- Information on how project communication is performing by comparing the communications that were implemented compared to those that were planned.
- It also considers feedback on communications, such as survey results on communication effectiveness.

Change requests

- Corrective actions
- Preventive actions

Project Management Plan updates

- Stakeholder Engagement Plan
- Communication Management Plan

Project documents updates

- Stakeholder register.
- Issue log.
- Lessons learned register.

Inputs

Work Performance Data

- Data of communications that have actually been distributed.

Project Management Plan

- Stakeholder Engagement Plan
- Communication management Plan
- Resource Management Plan

Project Documents

- **Project communications:** Deliverables status, Schedule progress, and Costs incurred.
- **Issue Log:** used to facilitate communication and ensure a common understanding of issues.

Enterprise environmental factors

- Global, regional, or local trends, practices, or habits; and
- Timezones, Geographic distribution of facilities and resources.

Organizational Process Assets


- Corporate policies and procedures f social media
- Organizational communication requirements;

BUT IT WASN'T UNTIL
I MAPPED OUT ALL OF
THE PARTY GUESTS IN A
POWER/INTEREST GRID
THAT I REALLY KNEW
HOW TO KEEP THEM
SATISFIED.



Stakeholder Management

Project management is about knowing your audience.

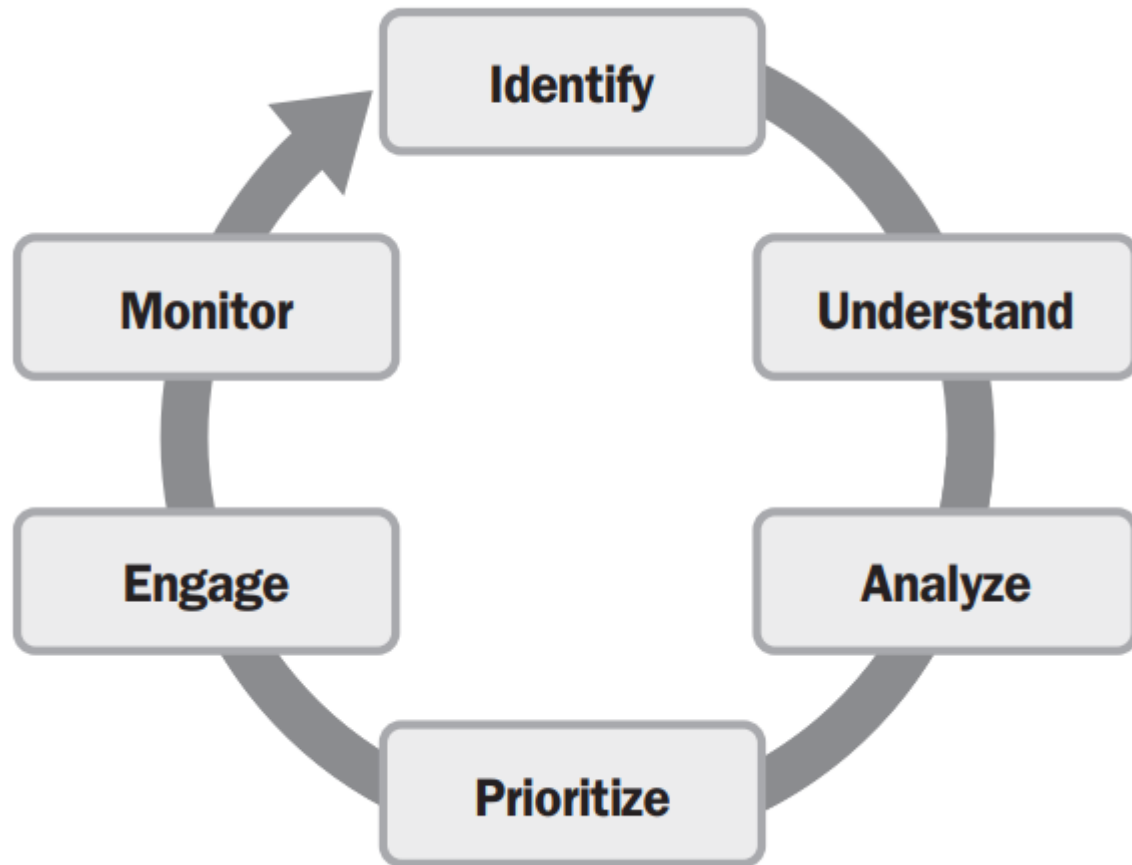

Manage Stakeholder Engagement

Manage Stakeholder Engagement


- **What:** communicating and working with stakeholders to meet their needs and expectations, address issues, and foster appropriate stakeholder involvement
- **Why:**
 - Ensure that stakeholders clearly understand the project goals, objectives, benefits, and risks for the project, as well as how their contribution will enhance project success
 - allows the project manager to increase support and minimize resistance from stakeholders
- **When:** performed throughout the project

Manage Stakeholder Engagement


- **How?**

- Engaging stakeholders at appropriate project stages to obtain, confirm, or maintain their continued commitment to the success of the project;
- Managing stakeholder expectations through negotiation and communication;
- Addressing any risks or potential concerns related to stakeholder management and anticipating future issues that may be raised by stakeholders
 - Issues
 - Changes
 - Risks
- Clarifying and resolving issues that have been identified

Process

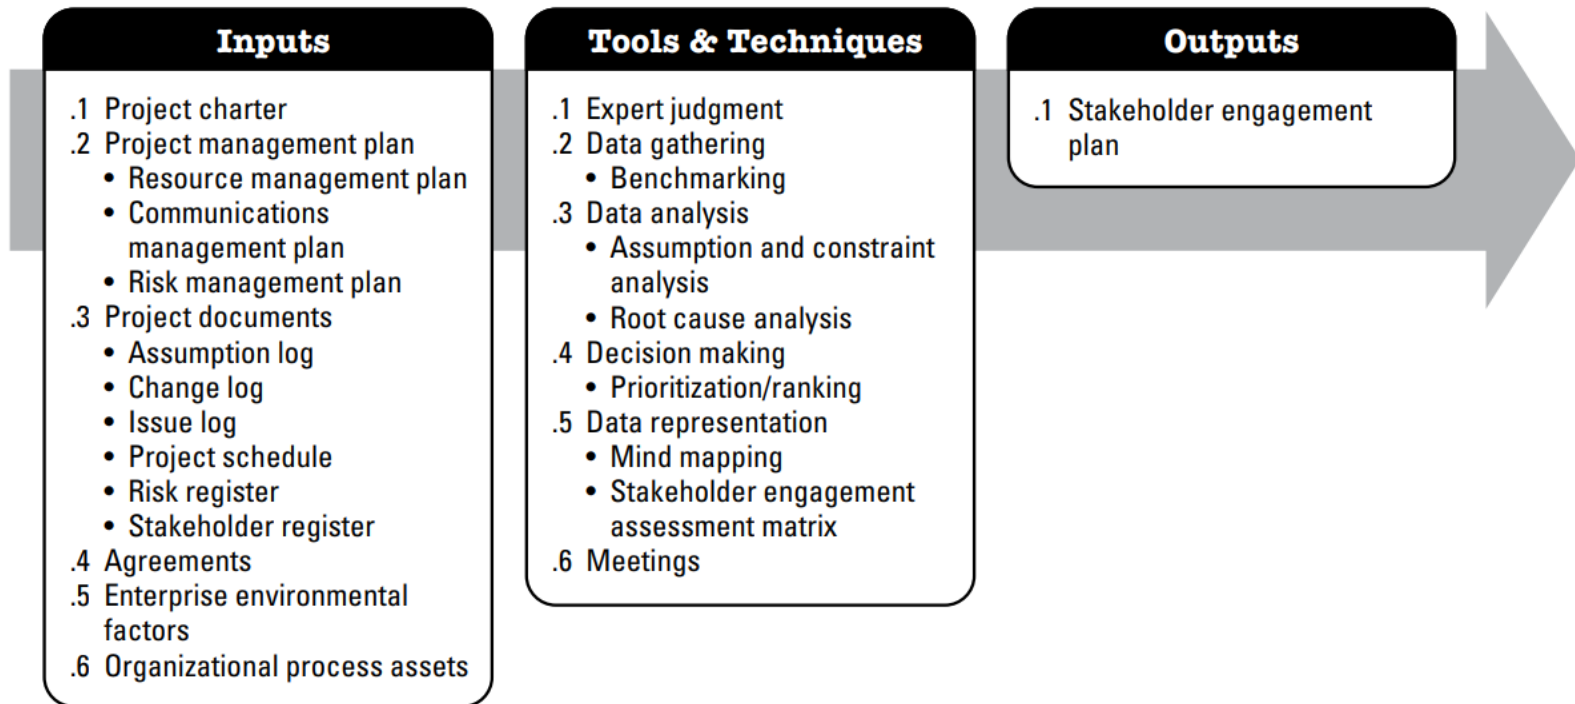


Data Flow

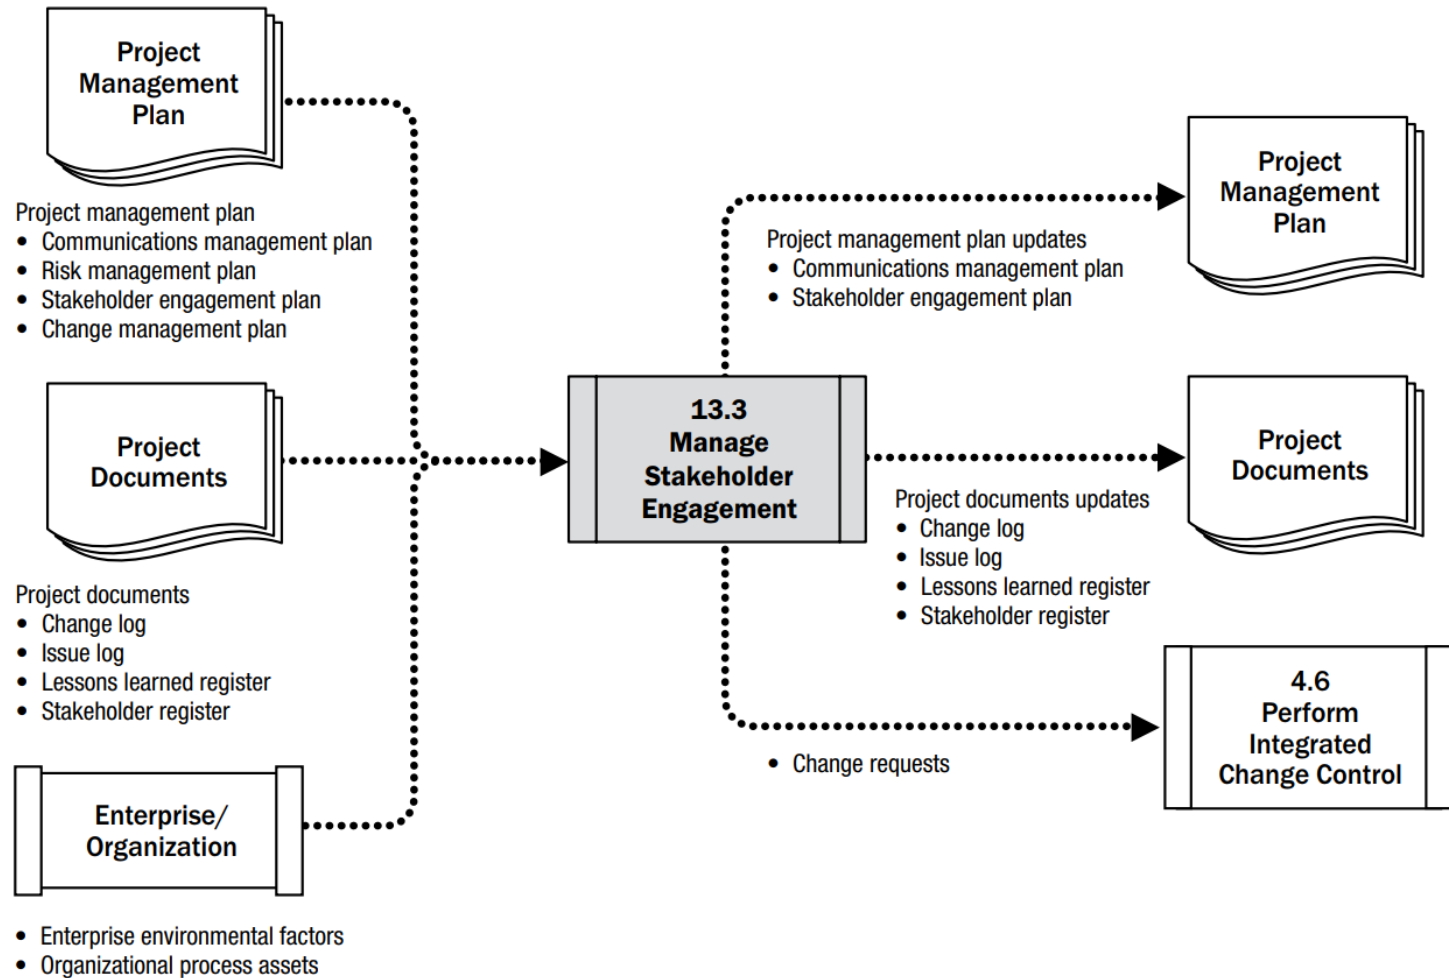

Tools & Techniques

Ground rules

- A set of expected behaviors that the team agrees to use them, as well as other stakeholders, with regard to stakeholder engagement.
- Ground rules help to reduce conflicts



Meeting

Meetings are used to discuss and address any issue or concern regarding stakeholder engagement.

- Issue resolution
- Lessons learned and retrospectives,
- Project kick-off
- Sprint planning
- uuStatus updates

Tools & Techniques

Interpersonal and team skills

- **Observation/conversation.** is used to stay in touch with the work and attitudes of project team members and other stakeholders.
- **Negotiation and Conflict management** is used to achieve support or agreement that supports the work of the project or its outcomes and to resolve conflicts within the team or with other stakeholders.
- **Cultural awareness:** is used to help the project manager and team to communicate effectively by considering cultural differences and the requirements of stakeholders.
- **Political awareness:** is achieved through understanding the power relationships within and around the project.



Tools & Techniques

Communication skills

- The methods of communication identified for each stakeholder in the communications management plan are applied during stakeholder engagement management.
- The project management team uses feedback to assist in understanding stakeholder reaction to the various project management activities and key decisions.
- **Feedback** may be collected in the following ways, but not limited to:
 - Conversations; both formal and informal,
 - Issue identification and discussion,
 - Meetings,
 - Progress reporting, and
 - Surveys

Types Of Communication Skills



Outputs

Change requests

- Change to project/product requirement and scope

Project Management Plan Updates

- Stakeholder Engagement Plan
- Communications management plan

Project Documents updates

- Stakeholder register.
- **Issue log**
- Change log
- Risk register
- Lessons learned register

Issue Logs

- Help project manager to document issues, define the impact, priority and urgency of the issues, assign ownership of those issues, and established due dates for resolution.


Monitor Stakeholder Engagement

*You **manage** to make things happen. You **monitor** to make sure things are happening the right way.*


Monitor Stakeholder Engagement

- **What:** monitoring project stakeholder relationships and tailoring strategies for engaging stakeholders through modification of engagement strategies and plans
- **Why:** maintains or increases the efficiency and effectiveness of stakeholder engagement activities as the project evolves and its environment changes
- **When:** performed throughout the project
- **How:**
 - Compare the results of current stakeholders engagement activities with the activities outlined in Stakeholder Engagement Plan
 - Identify and quantify any variances
 - Prioritise options and select the best response for a variance in stakeholder engagement.

Process

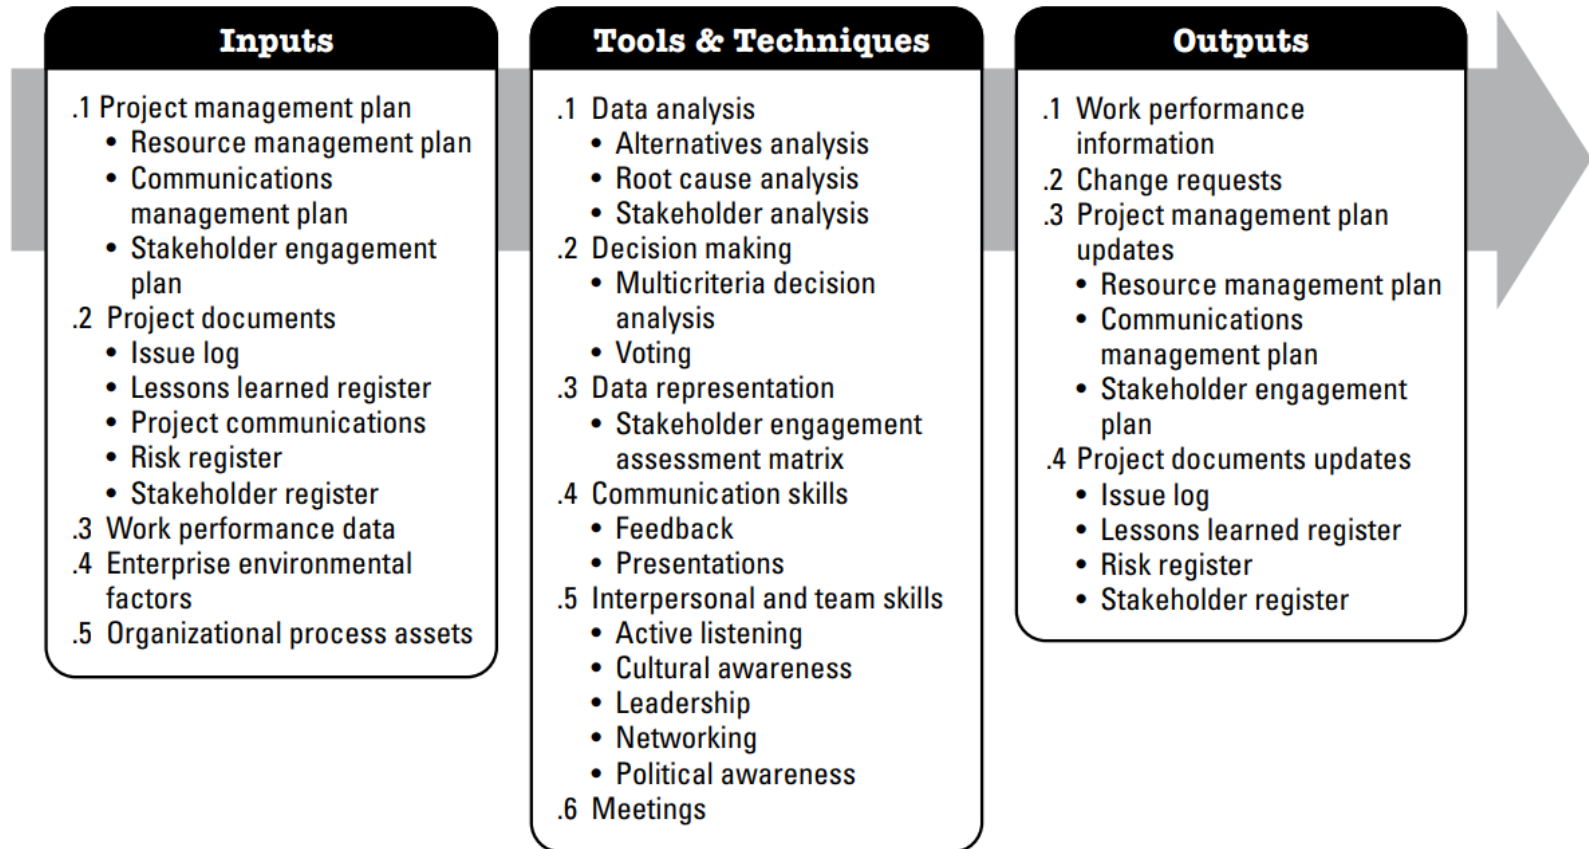


Data Flow

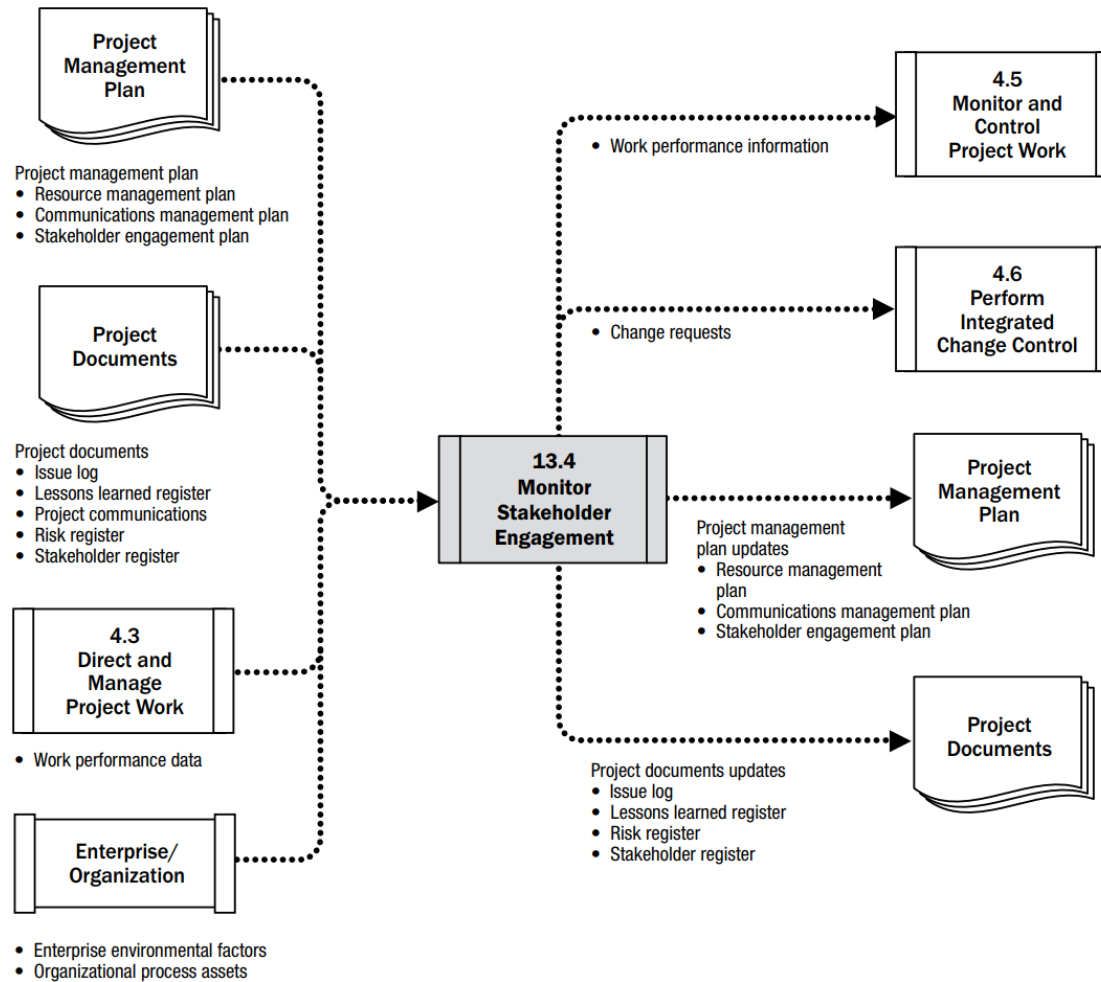

Tools & Techniques

Data analysis

- **Alternatives analysis:** evaluate options to respond to variances in the desired results of stakeholder engagement.
- **Root cause analysis:** determine the basic underlying reason that stakeholder engagement is not having the planned effect. Ex. Six Sigma, fishbone diagram,...
- **Stakeholder analysis:** determine the position of stakeholder groups and individuals at any particular time in the project.

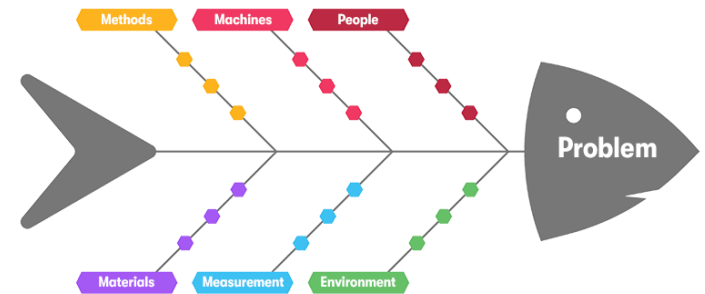

Stakeholder	Unaware	Resistant	Neutral	Supportive	Leading
Bob	C			D	
Carol			C		D
Ted		C		D	
Alice				C,D	
Joe			C	D	

Tools & Techniques

Interpersonal and team skills

- **Active listening.** Active listening is used to reduce misunderstandings and other miscommunication.
- **Leadership.** communicate the vision and inspire stakeholders to support the work and outcomes of the project.
- **Networking.** Networking ensures access to information about levels of engagement of stakeholders.
- **Cultural awareness.**
- **Political awareness.**



Tools & Techniques

Meetings

- Status review meetings are used to exchange and analyze information about stakeholder engagement.

Communication skills

- **Feedback.** Feedback is used to ensure that the information to stakeholders is received and understood.
- **Presentations.** Presentations provide clear information to stakeholders.



Outputs

Work performance information

- The status of stakeholder engagement

Change requests

- Corrective actions
- Preventive actions

Project management plan updates


- Stakeholder Engagement Plan
- Resource management plan
- Communications management plan,

Project documents updates

- Stakeholder register
- Issue log
- Change log
- Risk register
- Lessons learned register

Aspect	Manage Stakeholder Engagement	Monitor Stakeholder Engagement
Process Group	Executing	Monitoring & Controlling
Purpose (Meaning)	Actively work with stakeholders to meet their needs and expectations, address issues, and foster appropriate engagement.	Track overall stakeholder relationships, evaluate effectiveness of engagement strategies, and adjust plans if needed.
Focus	Doing – engaging and communicating with stakeholders.	Checking – measuring if engagement is working as intended.
Timing	During project execution , when stakeholder interactions happen.	Throughout the project, especially when issues arise or performance is reviewed.
Key Inputs	- Stakeholder engagement plan - Communications plan - Change log - Project documents - Project management plan	- Stakeholder engagement plan - Work performance data - Issue log - Project documents - Project management plan
Key Tools & Techniques	Communication methods; Interpersonal skills; Conflict management; Ground rules; Cultural awareness	Stakeholder engagement assessments; Data analysis; Decision making; Communication methods
Key Outputs	Change requests; Project document updates; Project management plan updates; Issue log updates	Work performance information; Change requests; Updates to project documents and plans
Example Activities	- Holding stakeholder meetings - Negotiating expectations - Solving conflicts - Sending status updates	- Reviewing stakeholder feedback - Comparing actual vs. planned engagement - Updating strategy based on assessment

Direct and Manage Project Work process

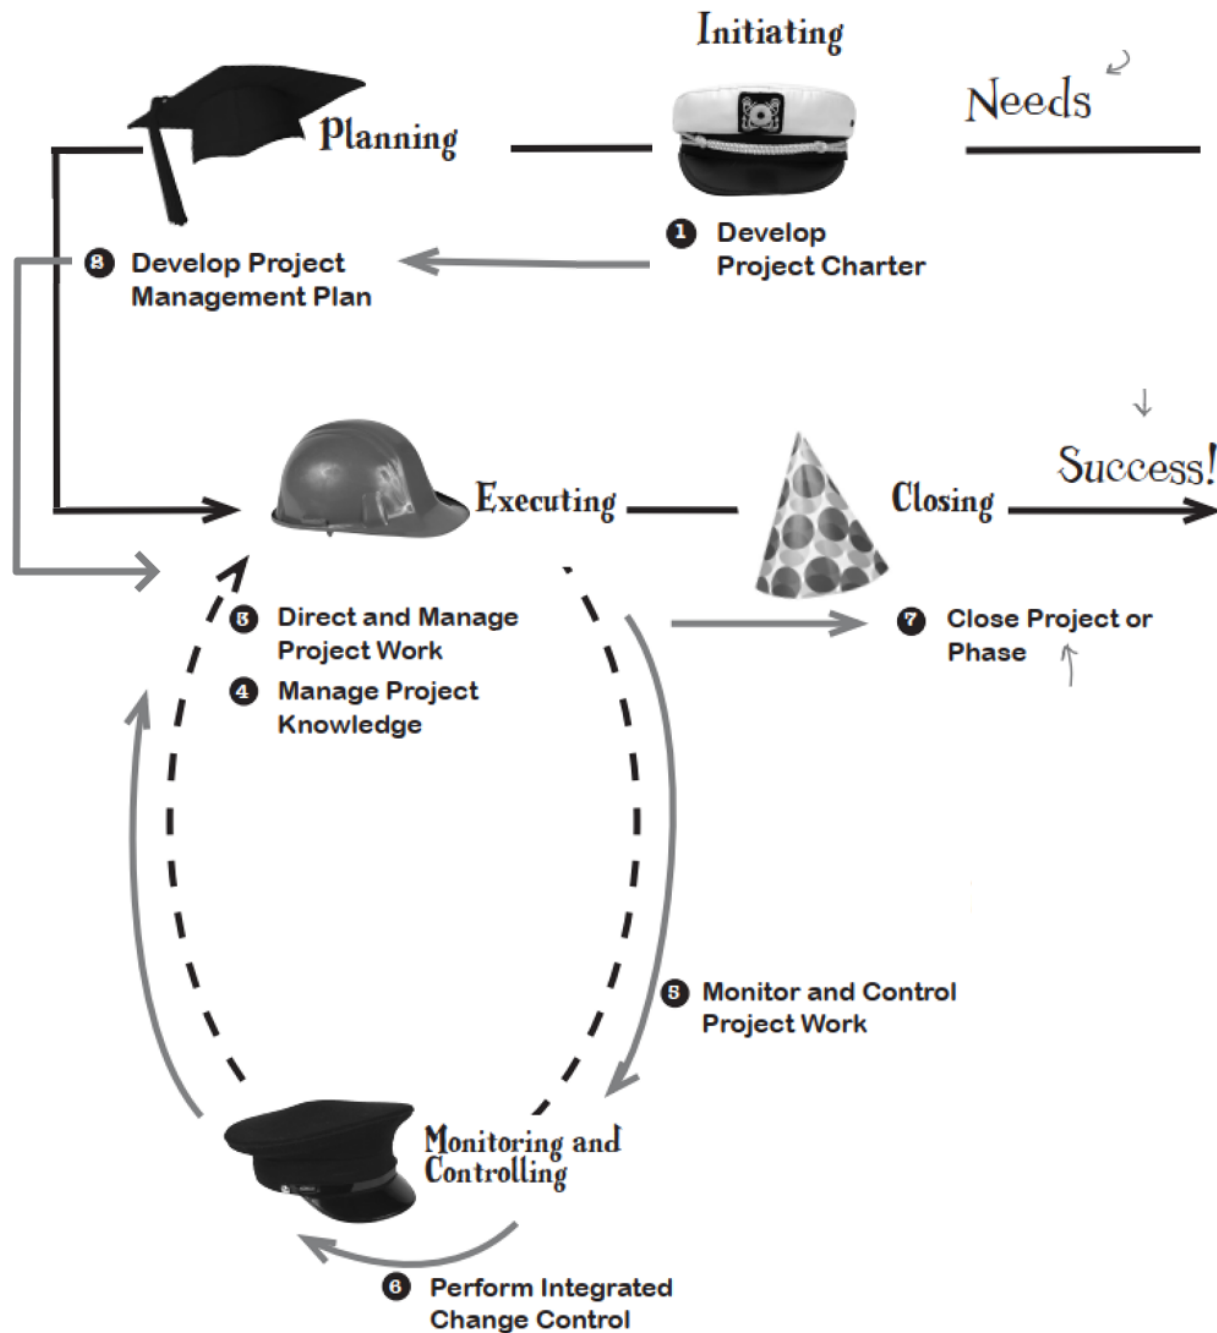

Direct and Manage Project Work

What?

- The process of leading and performing the work defined in the project management plan and
- Implementing approved changes to achieve the project's objectives.

Why?


- It provides overall management of the project work and deliverables, thus **improving the probability of project success**.


When?

- Throughout the project.




Direct and Manage Project Work

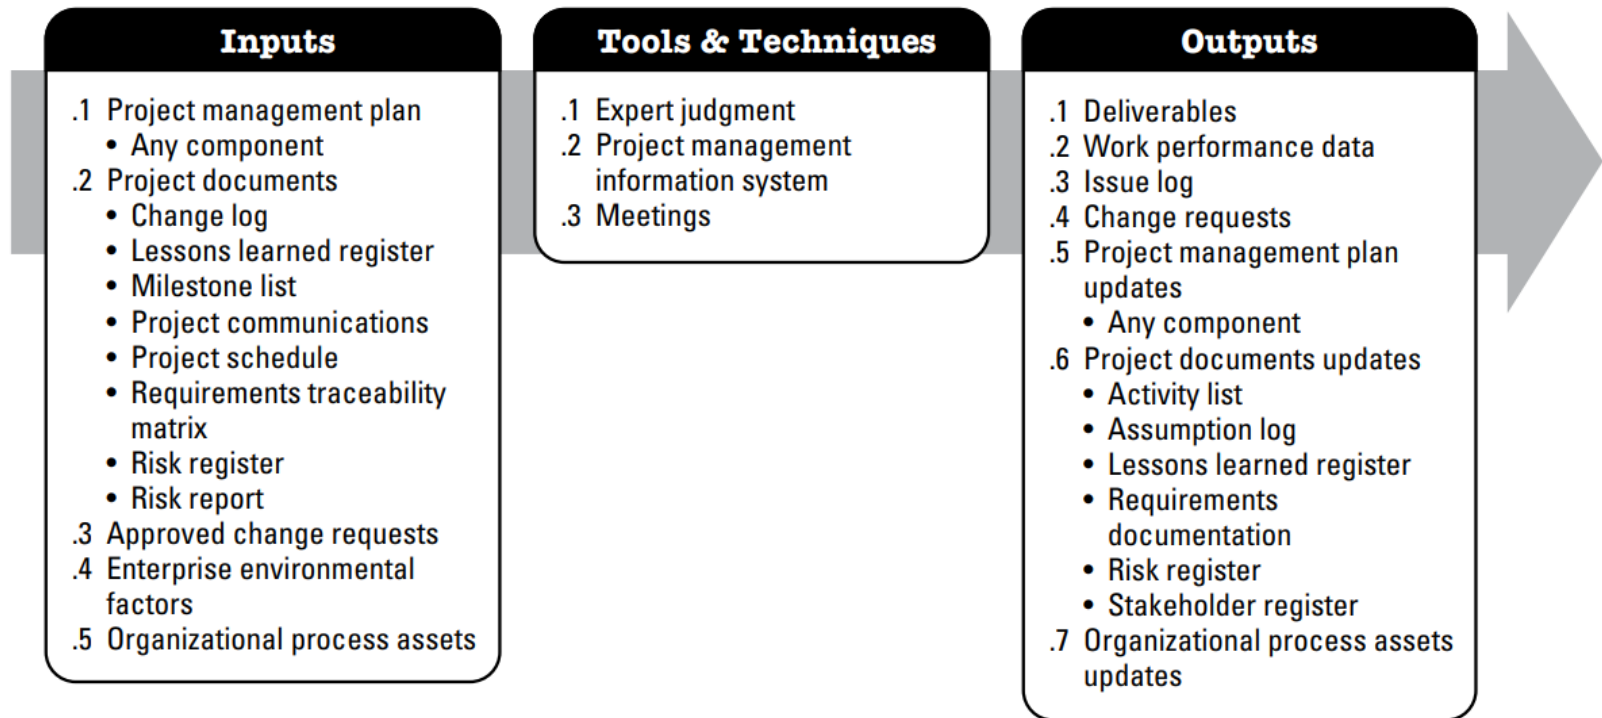

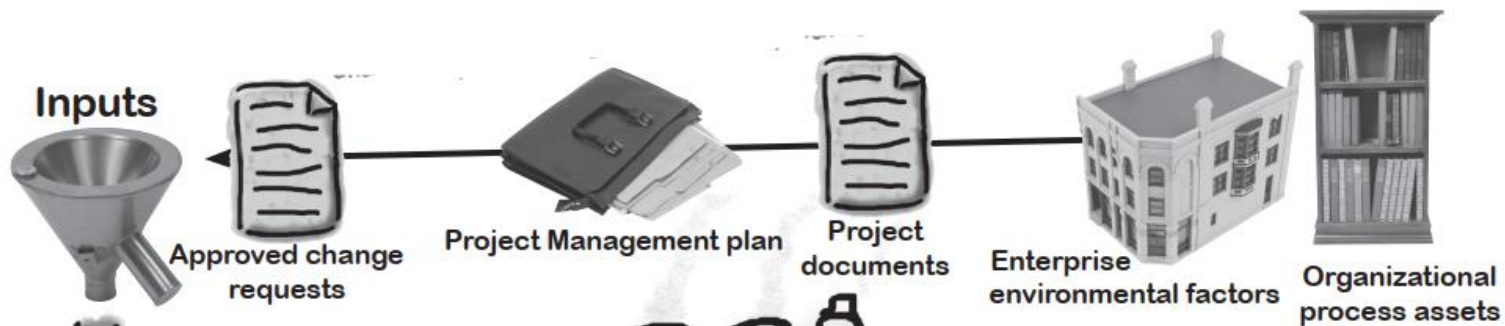

simply follow the plan you've put together and handle any problems that come up.

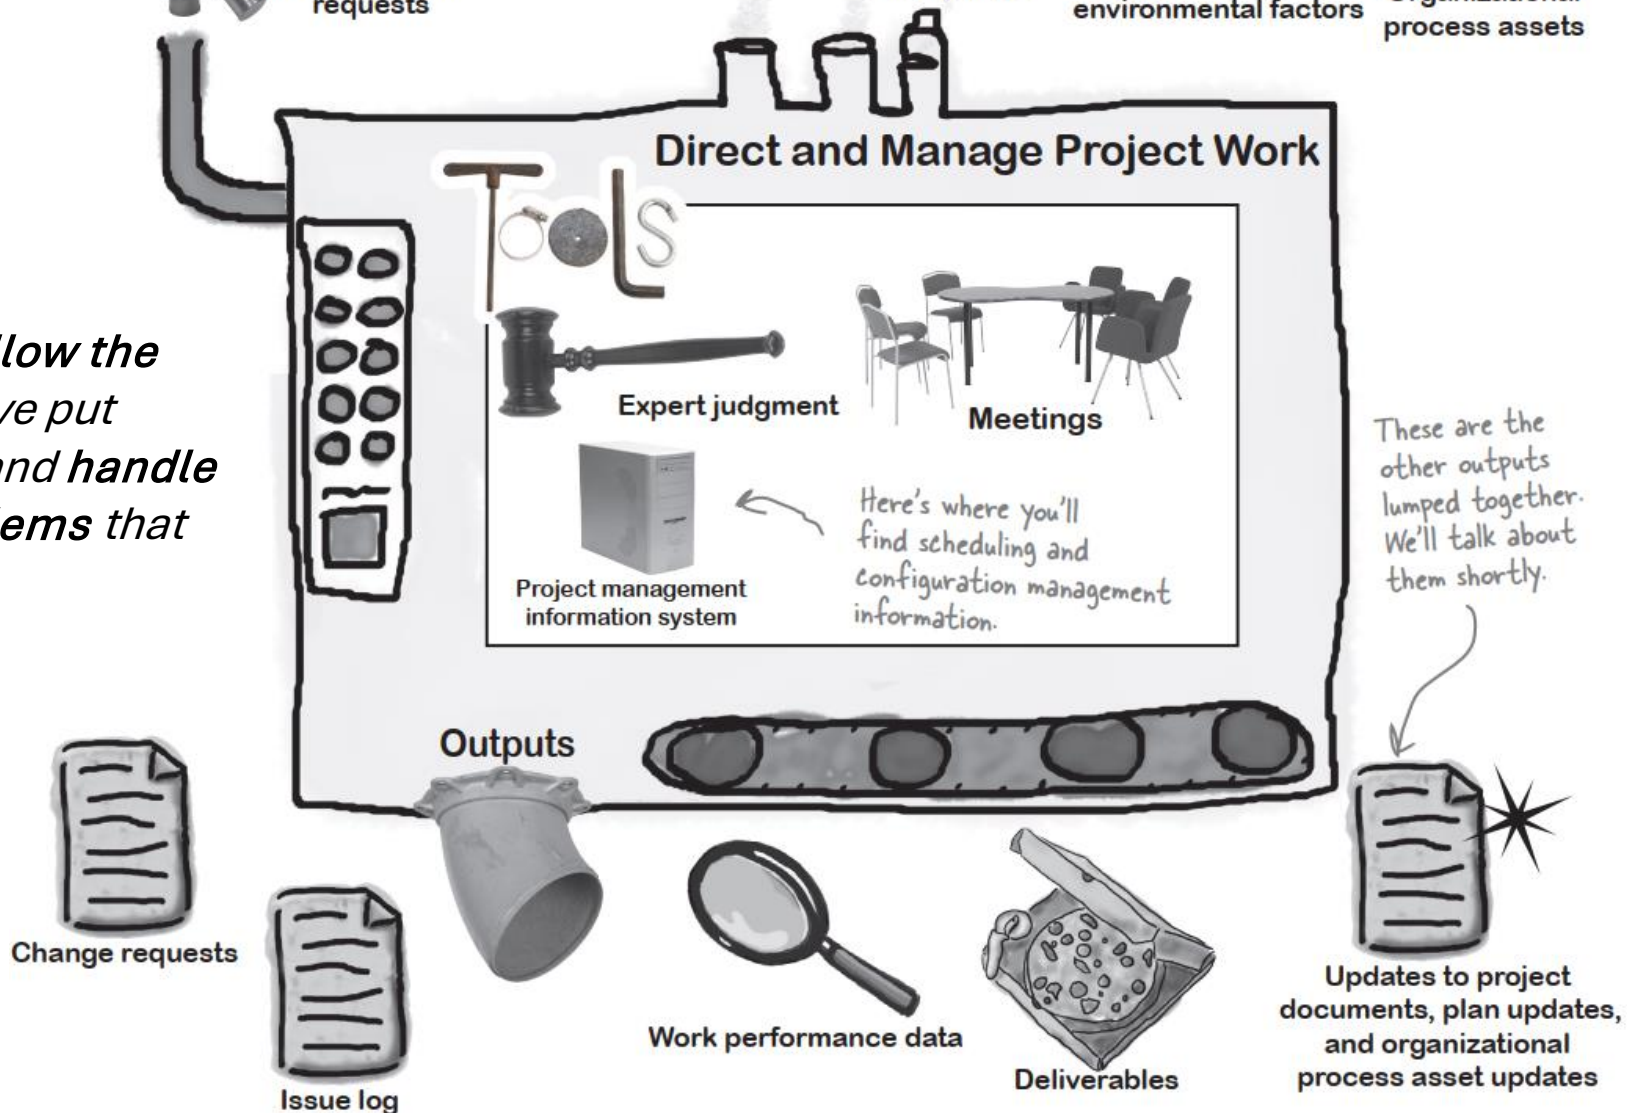

Inputs

Project management plan

- Any component of the project management plan may be an input to this process

Project documents

- Change log: contains the status of all change requests
- Lessons learned register
- Milestone list; Project schedule
- Requirements traceability matrix
- Risk register, risk reports...

Approved change requests

- may be a corrective action, a preventive
- action, or a defect repair.

Enterprise Environmental Factors

- Organizational structure, culture, management practices, and sustainability;
- Infrastructure (e.g., existing facilities and capital equipment);
- Stakeholder risk thresholds

Organizational Process Assets


- Issue and defect management procedures, database
- Change control and risk control procedures;
- Project information from previous projects

Tools & Techniques

Project Management Information System

The PMIS provides access to informat technology (IT) software tools:

- Information collection and distribution system
- Scheduling software tool
- Corporate knowledge base repositories.
- Work authorization system
- Configuration management system
- Change control system

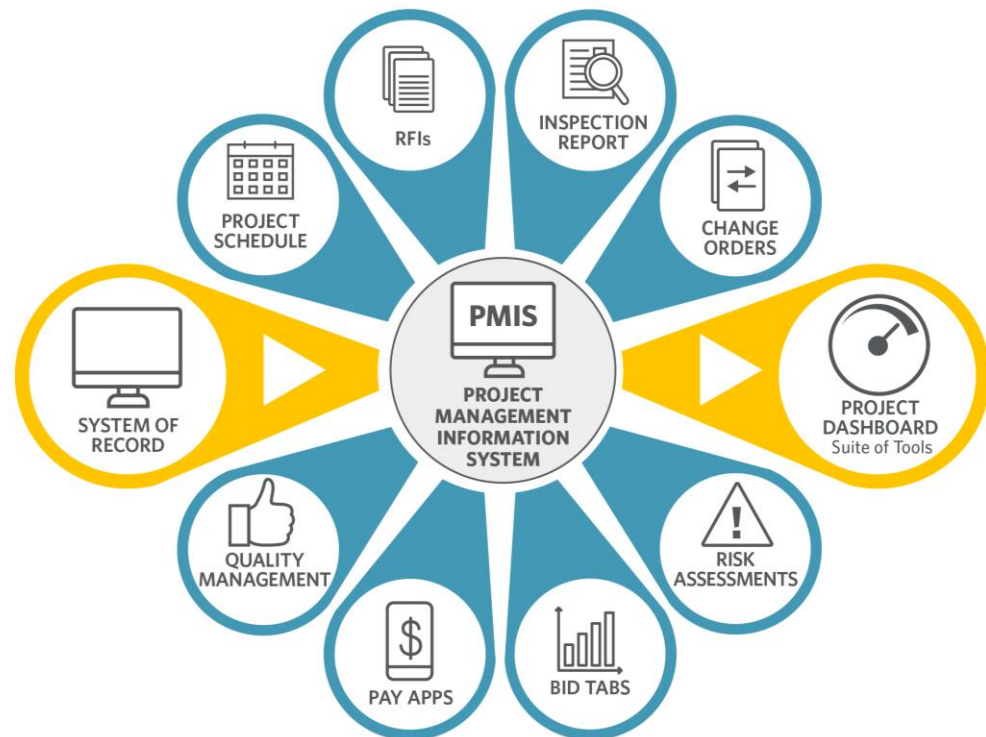

Popular PMIS

PMIS capabilities

- Work breakdown structure (WBS) planning
- Timeline and scheduling (Gantt, roadmap)
- Task tracking and progress management
- Resource assignment and permissions
- Resource management
- KPI reports, burndown charts
- Integration with development tools (Git, CI/CD) (sometimes)

PMIS limitations

- Real-time communication (chat, video): Not effective — use Slack, Discord, or Teams
- Document writing and collaboration: Better with Google Docs, Confluence
- Source code management & code review: Use GitHub, GitLab, Bitbucket
- CI/CD and test automation: Use Jenkins, GitHub Actions, GitLab CI
- Knowledge base or team wiki: Available but often limited — better with Notion or Confluence



Tools & Techniques

Expert judgment

- Expert judgment is used to assess the inputs needed to direct and manage execution of the project management plan
 - Technical knowledge
 - Cost and budget, procurement
 - Legislation and regulations, organizational governance.




Meeting

- Discuss and address pertinent topics of the project when directing and managing project work.
- Attendees may include the project manager, the project team, and appropriate stakeholders
- Type of meeting: kick-off, technical, sprint or iteration planning, problem solving, progress update...



Outputs

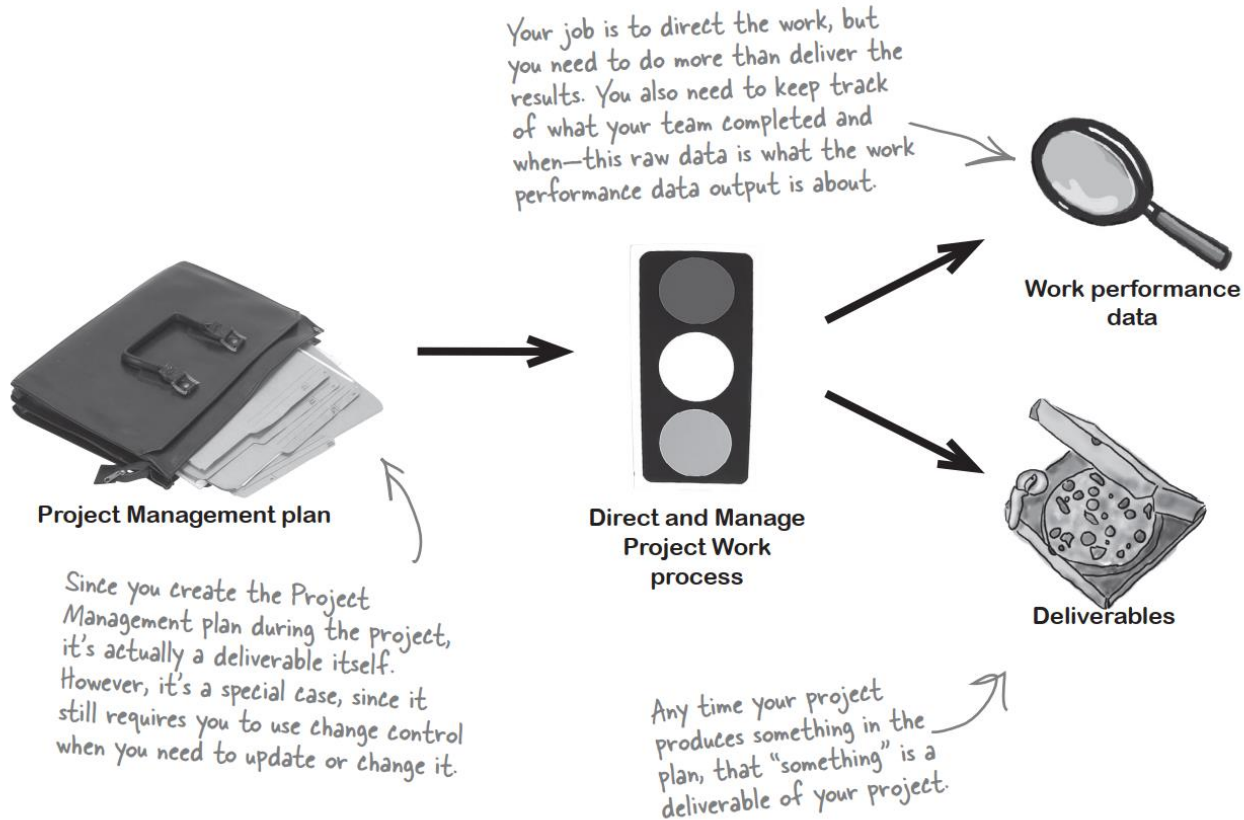


*You create **work performance data** by measuring how and when the processes from each knowledge area are being performed.*

Outputs

Deliverables

- Any **unique and verifiable** product, result, or capability to perform a service that is required to be produced to complete a process, phase, or project.
- Deliverables are **typically tangible** components completed to meet the project objectives
- And can include elements of the project management plan.
- Change control** should be applied once the first version of a deliverable has been completed.

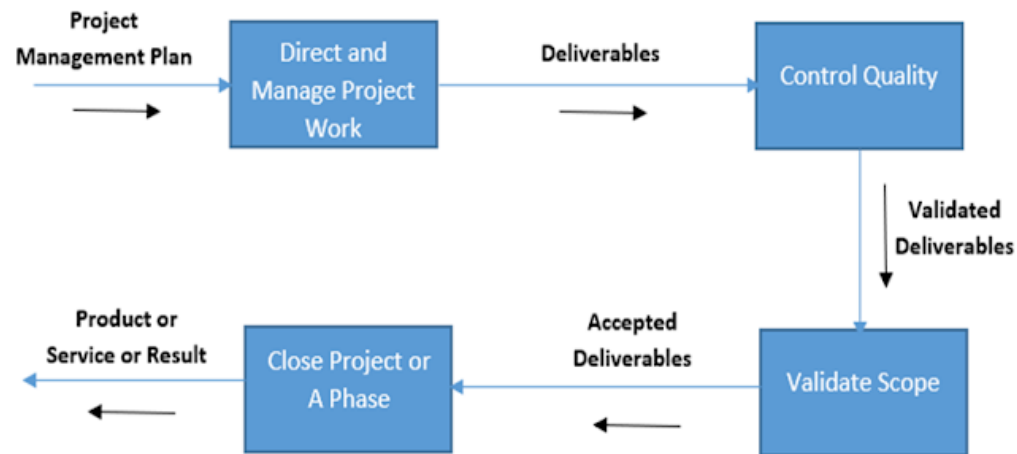

Copyright - Satya Narayan Dash. All Rights Reserved.

Outputs

Work Performance Data

The raw observations and measurements identified during activities being performed to carry out the project work. Ex:


- Work completed
- Key performance indicators
- Technical performance measures
- Start and finish dates of schedule activities,
- Number of change requests
- Number of defects
- Actual costs
- And actual durations
- Etc.



Outputs

Change Requests

- **Corrective actions:** that will bring anticipated project performance into compliance with the project management plan
- **Preventive actions:** to reduce the probability of potential negative consequences
- **Defect repair:** requests to correct product defects found by the quality process.
- **Updates.** Changes to formally controlled project documents, plans, etc., to reflect modified or additional ideas or content.



Outputs

Issue log

- The issue log is a project document where all the issues are recorded and tracked.
- The issue log will help the project manager effectively track and manage issues, ensuring that they are investigated and resolved.
- The issue log is created for the first time as an output of this process, although issues may happen at any time during the project.
- The issue log is updated as a result of the monitoring and control activities throughout the project's life cycle.

Project management plan updates

- Any component of the project management plan.

Project documents updates

- Stakeholder register
- Requirements documentation
- Assumption log
- Activity list
- Lessons learned register
- Risk register

Organizational process assets updates

3 main components of the Direct and Manage Project Work process

- Most of activities are implementing changes, repairs, and corrective action
 - Use the plan to **create deliverables**.
 - **Repair defects** in deliverables.
 - As the project plan **changes**, make sure those changes are reflected in the deliverables.
- **Deliverable**: anything that the project delivers
 - products or services that team are performing for the client, customer, or sponsor
 - include every single document, plan, schedule, budget, blueprint, and anything else that gets made along the way



Deliverables

Deliverables or work performance data?

1. The software project team builds software.

☐

Deliverable

☐

Work performance data

2. A builder hangs a door.

☐

Deliverable

☐

Work performance data

3. A wedding photographer sends the photo proofs to the client.

☐

Deliverable

☐

Work performance data

4. The cable repair technicians take an average of four hours per job.

☐

Deliverable

☐

Work performance data

5. The construction crew worked 46 hours of overtime in March.

☐

Deliverable

☐

Work performance data

6. The construction crew built the six houses required by the plan.

☐

Deliverable

☐

Work performance data

1. The software project team builds software.

☒ Deliverable

☐ Work performance data

2. A builder hangs a door.

☒ Deliverable

☐ Work performance data

3. A wedding photographer sends the photo proofs to the client.

☒ Deliverable

☐ Work performance data

4. The cable repair technicians takes an average of four hours per job.

☐ Deliverable

☒ Work performance data

5. The construction crew worked 46 hours of overtime in March.

☐ Deliverable

☒ Work performance data

6. The construction crew built the six houses required by the plan.

☒ Deliverable

☐ Work performance data
